

Project : 022656.00(0)

FRENCHVILLE-FORT KENT, ROUTE 1

						22	24	26	28	
Activity Name	Activity Description	Rem. Dur.	Orig. Dur.	Early Start	Early Finish	actual finish date				
X01	PROJECT KICKOFF	0	0			12Jul15				
X02	COACHPOINT 1	0	0			13Jul15				
A01	Activate PCE Funds	0	1			13Jul15				
A03	Project Management: Preliminary Engineering Phase	1	335		13Apr22					
R35	Existing R/W & Ownership	0	158			18Dec15				
D26	Preliminary Data Gathering	0	15			28Jul15				
A04	Initial Contacts: Town, Feds and/or MPO's	0	5			18Jul15				
R39	Initial Utility Contacts	0	30			12Aug15				
S45	Preliminary Survey	0	165			25Dec15				
G25	Preliminary Subsurface Investigation	0	10			23Jul15				
E41	Phase I Environmental Evaluation	0	25			07Aug15				
X07	INITIAL TEAM MEETING	0	0			13Aug16				
R36	Plot Existing R/W & Property Lines	0	128			19Dec16				
E42	Phase II Environmental Evaluation	0	125			16Dec16				
D25	Preliminary Drainage Design	0	121			12Dec16				
T20	Preliminary Traffic Design	0	105			26Nov16				
R38	Preliminary Utility Coordination	0	97			18Nov16				
G45	Preliminary Geotechnical Information	0	100			21Nov16				
E40.1	DRAFT BA	0	85			09Dec16				
D20	Preliminary Alignment Design	0	200			07Dec17				
X11	PRELIMINARY ALIGNMENT COMPLETE	0	0			26Jul18				
X14	COACHPOINT 2	0	0			26Jul18				
E43	Phase III Environmental Evaluation	0	25			20Aug18				
R40	Assess Utility R/W Needs	0	15			10Aug18				
D30	Preliminary Structural Design	0	10			05Aug18				
R77	Relocation Planning	0	25			20Aug18				
D35	Preliminary Plan Development	0	40			04Sep18				
R37	Preliminary R/W Mapping	0	20			30Aug18				
A06	Municipal Funding Coordination	0	10			14Sep18				
D36	Preliminary Construction Estimate	0	5			09Sep18				

Project : 022656.00(0)


FRENCHVILLE-FORT KENT, ROUTE 1

						22	24	26	28		
Activity Name	Activity Description	Rem. Dur.	Orig. Dur.	Early Start	Early Finish	actual finish date					
R45	Major Impacts Complete	0	96			19Mar19					
X12	DRAFT PDR DISTRIBUTION	0	0			02Feb22					
X13	PDR/PRELIMINARY PLAN COMPLETE	0	0	13Apr22	13Apr22						
E40.2	BA REVIEW	15	15	14Apr22	04May22						
A05	Project Management: Final Engineering Phase	722	357	14Apr22	04Apr24						
X15	FORMAL PUBLIC MEETING	0	0	27Apr22	27Apr22						
R78	Relocation Implementation	40	40	28Apr22	06Jun22						
A09	Municipal Agreements	10	10	28Apr22	07May22						
E40.3	AGENCY REVIEW	100	100	05May22	21Sep22						
X17	MIDWAY TEAM MEETING	0	0	25May22	25May22						
G50	Final Geotechnical Design Report	40	40	26May22	04Jul22						
T25	Final Traffic Design	15	15	26May22	09Jun22						
D45	Final Highway Design	155	155	26May22	27Oct22						
E51	Phase I Environmental Coordination	30	30	26May22	24Jun22						
X10	SECTION 7 SIGNOFF	0	0	21Sep22	21Sep22						
X21	PLAN IMPACTS COMPLETE	0	0	27Oct22	27Oct22						
R53	R/W Mapping	150	150	28Oct22	26Mar23						
R50	Utilities Final Coordination	257	257	28Oct22	11Jul23						
D65	Final Estimate and Review	20	20	28Oct22	16Nov22						
S55	Construction Survey	30	30	28Oct22	26Nov22						
R32	Preparation of Titles	100	100	17Nov22	24Feb23						
A11	Construction Funding Requested	1	1	17Nov22	17Nov22						
D70	Design Package Complete	0	0	16Nov22	16Nov22						
X16	NEPA COMPLETE	0	0	08Dec22	08Dec22						
E52	Phase II Environmental Coordination	257	257	09Dec22	22Aug23						
R32.1	Verification of Titles	120	120	27Mar23	24Jul23						
R65	R/W Valuation	175	175	21May23	11Nov23						
R53.1	Final R/W Maps	20	20	25Jul23	13Aug23						
X23	UTILITIES CERTIFIED	0	0	22Aug23	22Aug23						
X24	ENVIRONMENTAL APPROVALS COMPLETE	0	0	22Aug23	22Aug23						

Project : 022656.00(0)

FRENCHVILLE-FORT KENT, ROUTE 1

						22	24	26	28		
Activity Name	Activity Description	Rem. Dur.	Orig. Dur.	Early Start	Early Finish	actual finish date					
A13	PS&E Reviewed by Contracts	7	7	23Aug23	29Aug23						
B4	Program Estimate Review	5	5	22Sep23	28Sep23						
R68	R/W Negotiation	70	70	12Nov23	20Jan24						
R74	R/W Condemnation & Acquisition	30	30	21Jan24	19Feb24						
TA2	Final TAME	0	0	25Jan24	25Jan24						
X25	R/W CERTIFIED	0	0	26Feb24	26Feb24						
X35	PS&E COMPLETE	0	0	07Mar24	07Mar24						
E53	Phase III Environmental Coordination	14	14	08Mar24	21Mar24						
A07	Project Management: Construction Phase	1766	1200	05Apr24	03Feb29						
X39	PROJECT ADVERTISED	0	0	04Apr24	04Apr24						
X40	LOCAL BILLING #1	0	0	04Apr24	04Apr24						
X43	CONTRACT DATE	0	0	04May24	04May24						
C25	Pre-Construction Approvals	30	30	05May24	03Jun24						
C30	Construction Administration	1656	1656	05May24	15Nov28						
A15	Pre-Construction Meeting	1	1	04Jun24	04Jun24						
X45	CONSTRUCTION BEGIN	0	0	04Jun24	04Jun24						
X46	LOCAL BILLING #2	0	0	10Aug26	10Aug26						
X47	FINAL TEAM MEETING/INSPECTION	0	0	15Nov28	15Nov28						
X49	CONSTRUCTION COMPLETE	0	0	15Nov28	15Nov28						
C50	Final Construction Documentation	60	60	16Nov28	14Jan29						
A17	Utility/Railroad Agreement Resolutions	5	5	15Jan29	19Jan29						
A19	R/W Dispute Resolutions	20	20	15Jan29	03Feb29						
X50	LOCAL BILLING #3	0	0	03Feb29	03Feb29						
A21	PROJECT COMPLETE	0	0	03Feb29	03Feb29						
X49C01	Physical Work Complete Letter Sent	0_W	0_W	13Feb29	13Feb29						
X49C03	106 Memo	0_W	0_W	15Mar29	15Mar29						
X49C05	Buy America Cert	0_W	0_W	15Mar29	15Mar29						
X49C07	Material Certs	0_W	0_W	15Mar29	15Mar29						
X49C09	DBE Signoff	0_W	0_W	15Mar29	15Mar29						
X49C11	Final Acceptance	0_W	0_W	29Mar29	29Mar29						

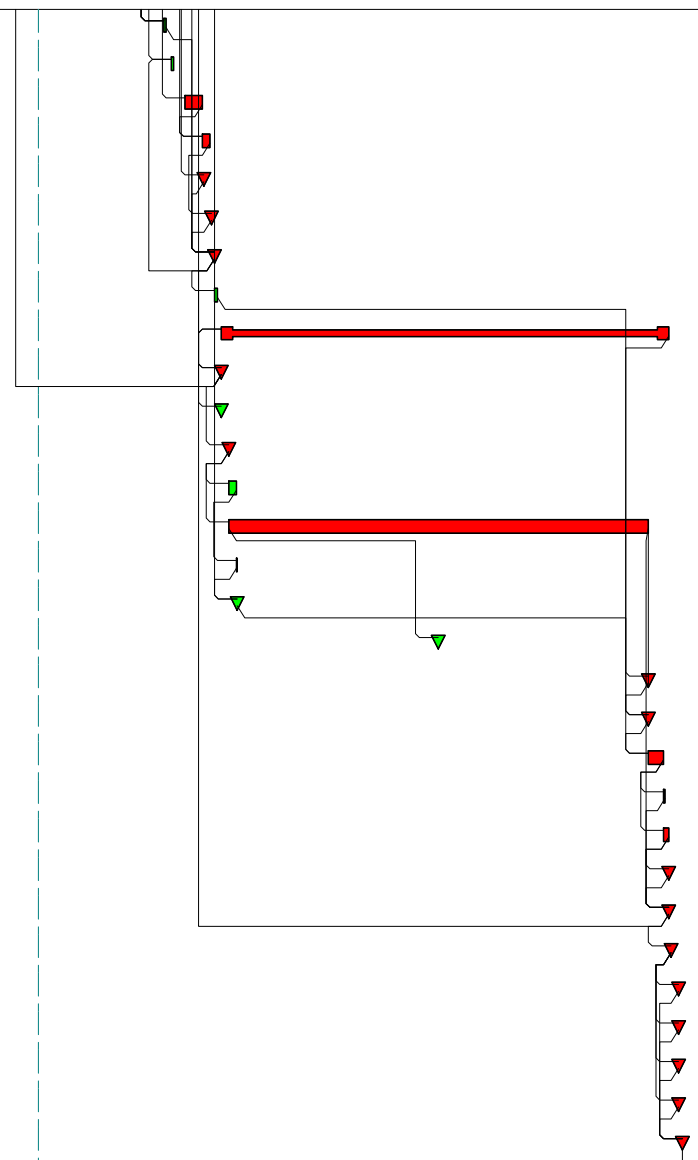

Project : 022656.00(0)

FRENCHVILLE-FORT KENT, ROUTE 1

							22	24	26	28	
Activity Name	Activity Description	Rem. Dur.	Orig. Dur.	Early Start	Early Finish	actual finish date					
X49C13	Final Records Submitted	0_W	0_W	27Jun29	27Jun29						
X49C15	Final Quantities Sent	0_W	0_W	11Jul29	11Jul29						
X49C17	All Bills Paid By Contractor	0_W	0_W	10Aug29	10Aug29						
X49C19	Agreement W/Final Quantities	0_W	0_W	10Aug29	10Aug29						
X49C21	Request for Final Payment Recieved	0_W	0_W	10Aug29	10Aug29						
X49C23	Other Need from Contractor	0_W	0_W	10Aug29	10Aug29						
XFINAL	Final Payment Made to Contractor	0_W	0_W	31Aug29	31Aug29						
X49C25	Commision Record/Final	0_W	0_W	30Sep29	30Sep29						
X49C27	Finals Folder Scanned	0_W	0_W	30Oct29	30Oct29						
X49C29	Final Plans Filed and Registered	0_W	0_W	15Oct30	15Oct30						
X49C31	All Titles Settled	0_W	0_W	15Oct30	15Oct30						
TA1	Draft TAME	0	0	22Oct30	22Oct30						
X49C99	Final Closed	0_W	0_W	22Oct30	22Oct30						

