


Appendix D

Project : 023094.00(0)


LITCHFIELD-WEST GARDINER, BABCOCK BR #2029

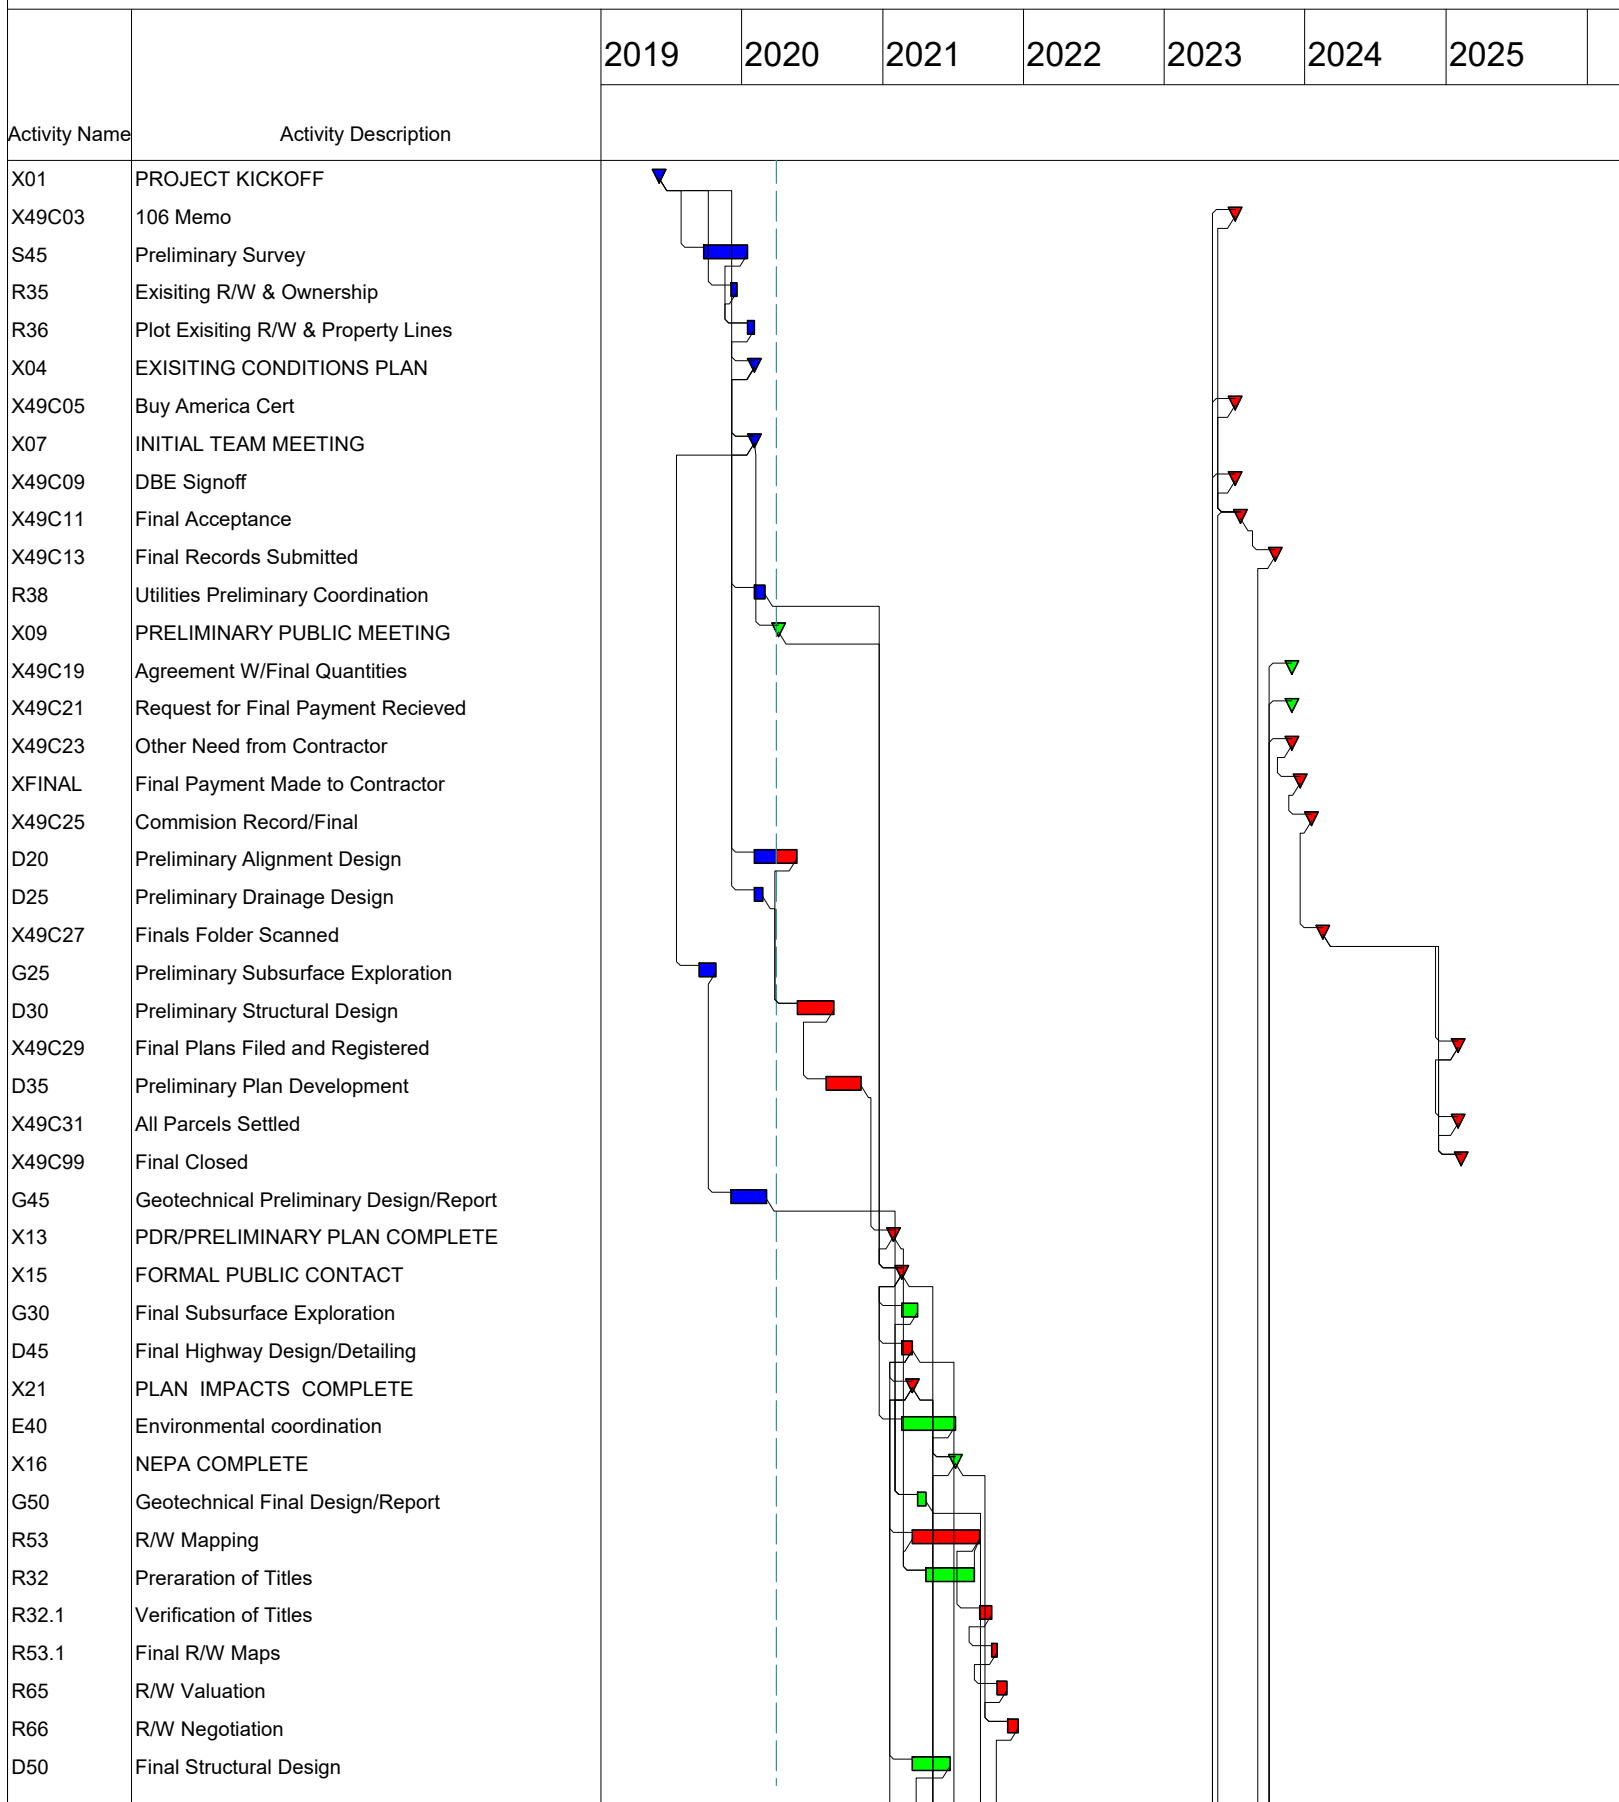


Project : 023094.00(0)

LITCHFIELD-WEST GARDINER, BABCOCK BR #2029

		2019	2020	2021	2022	2023	2024	2025	
Activity Name	Activity Description								
D55	Final Structural Plan Development			■					
D65	Final Estimate/Review			■					
R50	Utilities Final Coordination			■					
X23	UTILITIES CERTIFIED			▼					
R74	R/W Condemnation/Acquisition				■				
X24	ENVIRONMENTAL COMPLETE PACKAGE(ECR)			▼					
X25	R/W CERTIFIED				▼				
D70	PS&E REVIEW				■				
X35	PS&E COMPLETE				▼				
X39	PROJECT ADVERTISED				▼				
X43	CONTRACT DATE				▼				
X45	CONSTRUCTION BEGIN				▼				
C30	Construction Administration				■	■			
X49	CONSTRUCTION COMPLETE					▼			
X49C01	Physical Work Complete Letter Sent					▼			
X49C07	Material Certs					▼			
X49C15	Final Quantities Sent					▼			
X49C17	All Bills Paid By Contractor						▼		

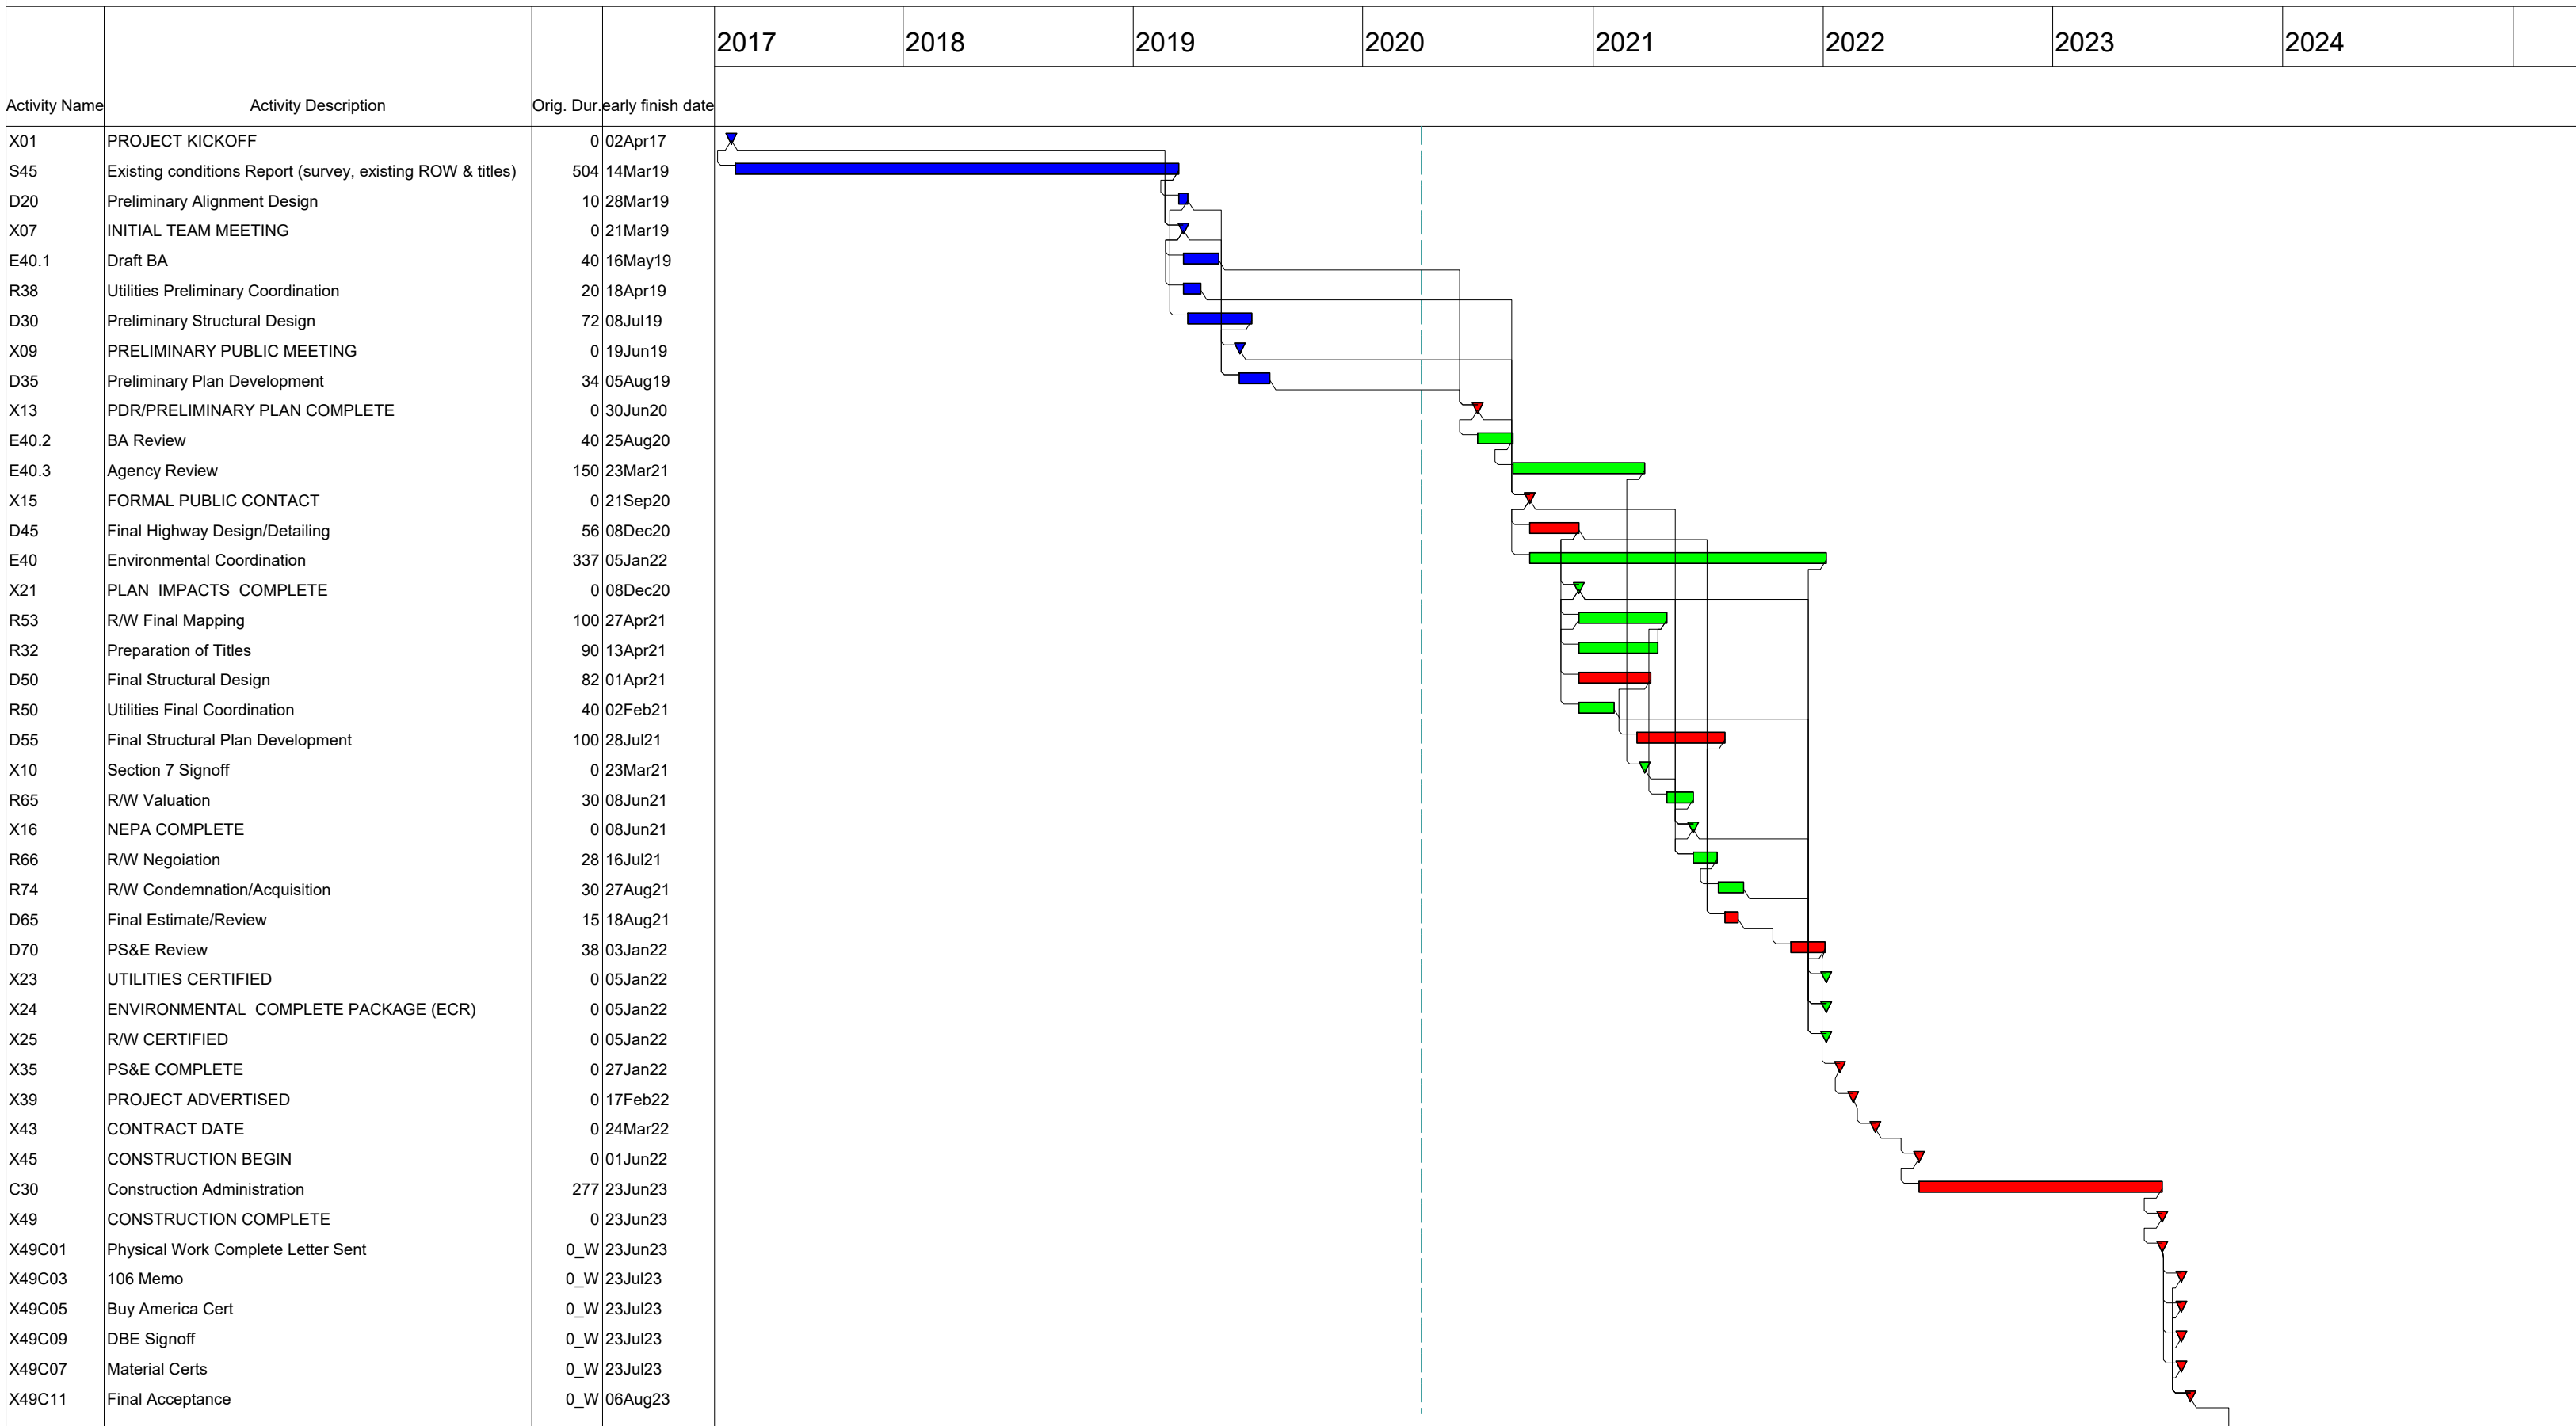

				2017	2018	2019	2020	2021	2022	2023	2024		
Activity Name	Activity Description	Orig. Dur.	early finish date										
X49C13	Final Records Submitted	0_W	04Nov23										
X49C15	Final Quantities Sent	0_W	18Nov23										
X49C19	Agreement W/Final Quantities	0_W	18Dec23										
X49C21	Request for Final Payment Recieved	0_W	18Dec23										
X49C23	Other Need from Contractor	0_W	18Dec23										
X49C17	All Bills Paid By Contractor	0_W	18Dec23										
XFINAL	Final Payment Made to Contractor	0_W	08Jan24										
X49C25	Commision Record/Final	0_W	07Feb24										
X49C27	Finals Folder Scanned	0_W	08Mar24										
X49C29	Final Plans Filed and Registered	0_W	21Feb25										
X49C31	All Titles Settled	0_W	21Feb25										
X49C99	Final Closed	0_W	28Feb25										

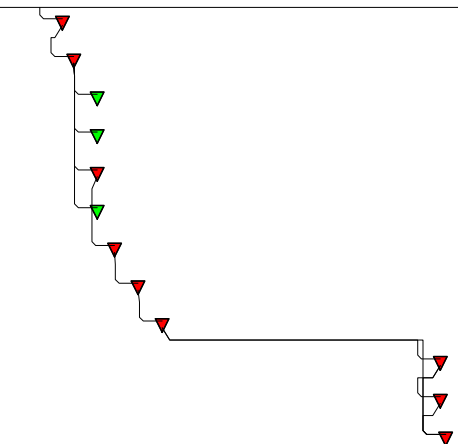

Project : 021727.00(0)

GREENBUSH, Boom Bridge #3587

								2018	2019	2020
Activity Name	Activity Description	Rem. Dur.	Orig. Dur.	actual start date	actual finish date	Early Start	Early Finish			
X01	PROJECT KICKOFF	0	0	14Apr16	14Apr16					
X49C03	106 Memo	0_W	0_W			01Dec24	01Dec24			
S45	Existing Conditions Report (survey, PORs & existing ROW)	0	90	15Apr16	18Aug16					
X49C05	Buy America Cert	0_W	0_W			01Dec24	01Dec24			
X07	INITIAL TEAM MEETING	0	0	03May17	03May17					
X49C09	DBE Signoff	0_W	0_W			01Dec24	01Dec24			
E40.1	Draft BA	0	40	21Oct16	15Dec16					
X49C13	Final Records Submitted	0_W	0_W			15Mar25	15Mar25			
R38	Utilities Preliminary Coordination	0	20	21Oct16	17Nov16					
X09	PRELIMINARY PUBLIC MEETING	0	0	03May17	03May17					
X49C19	Agreement W/Final Quantities	0_W	0_W			28Apr25	28Apr25			
X49C21	Request for Final Payment Recieved	0_W	0_W			28Apr25	28Apr25			
X49C23	Other Need from Contractor	0_W	0_W			28Apr25	28Apr25			
XFINAL	Final Payment Made to Contractor	0_W	0_W			19May25	19May25			
X49C25	Commision Record/Final	0_W	0_W			18Jun25	18Jun25			
D20	Preliminary Alignment Design	0	20	19Aug16	15Sep16					
D25	Preliminary Drainage Design	0	20	19Aug16	15Sep16					
X49C27	Finals Folder Scanned	0_W	0_W			18Jul25	18Jul25			
G25	Preliminary Subsurface Exploration	0	30	21Oct16	01Dec16					
D30	Preliminary Structural Design	0	140	16Sep16	30Mar17					
X49C29	Final Plans Filed and Registered	0_W	0_W			03Jul26	03Jul26			
D35	Preliminary Plan Development	137	260	14Apr17			18Sep20			
X49C31	All Titles Settled	0_W	0_W			03Jul26	03Jul26			
X49C99	Final Closed	0_W	0_W			10Jul26	10Jul26			
G45	Geotechnical Preliminary Design/Report	0	35	01Jun18	19Jul18					
X13	PDR/PRELIMINARY PLAN COMPLETE	0	0			02Oct20	02Oct20			
E40.2	BA review	60	60			05Oct20	25Dec20			
E40.3	Agency Review	135	135			28Dec20	02Jul21			
X10	Section 7 Signoff	0	0			02Jul21	02Jul21			
X15	FORMAL PUBLIC CONTACT	0	0			06Nov20	06Nov20			



Project : 021727.00(0)


GREENBUSH, Boom Bridge #3587

								2018	2019	2020
Activity Name	Activity Description	Rem. Dur.	Orig. Dur.	actual start date	actual finish date	Early Start	Early Finish			
G30	Final Subsurface Exploration	30	30			09Nov20	18Dec20			
D45	Final Highway Design/Detailing	120	120			09Nov20	23Apr21			
X21	PLAN IMPACTS COMPLETE	0	0			23Apr21	23Apr21			
X16	NEPA COMPLETE	0	0			02Jul21	02Jul21			
G50	Geotechnical Final Design/Report	25	25			26Apr21	28May21			
R53	R/W Final Mapping	135	135			26Apr21	29Oct21			
R32	Preparation of Titles	75	75			28Jun21	08Oct21			
R65	R/W Valuation	45	45			01Nov21	31Dec21			
R66	R/W Negotiation	30	30			03Jan22	11Feb22			
D50	Final Structural Design	135	135			05Apr21	08Oct21			
D55	Final Structural Plan Development	110	110			11Oct21	11Mar22			
D65	Final Estimate/Review	40	40			07Mar22	29Apr22			
R50	Utilities Final Coordination	60	60			26Apr21	16Jul21			
X23	UTILITIES CERTIFIED	0	0			25Mar22	25Mar22			
R74	R/W Condemnation/Acquisition	30	30			14Feb22	25Mar22			
R77	R/W Relocation Implementation	90	90			01Nov21	04Mar22			
E40	Environmental Evaluation	120	120			09Nov20	23Apr21			
X24	ENVIRONMENTAL COMPLETE PACKAGE (ECP)	0	0			02Jul21	02Jul21			
X25	R/W CERTIFIED	0	0			25Mar22	25Mar22			
D70	PS&E REVIEW	25	25			02May22	03Jun22			
X35	PS&E COMPLETE	0	0			03Jun22	03Jun22			
X39	PROJECT ADVERTISED	0	0			22Jun22	22Jun22			
X43	CONTRACT DATE	0	0			10Aug22	10Aug22			
X45	CONSTRUCTION BEGIN	0	0			08Sep22	08Sep22			
C30	Construction Administration	560	560			09Sep22	01Nov24			
X49	CONSTRUCTION COMPLETE	0	0			01Nov24	01Nov24			
X49C01	Physical Work Complete Letter Sent	0_W	0_W			01Nov24	01Nov24			
X49C07	Material Certs	0_W	0_W			01Dec24	01Dec24			
X49C11	Final Acceptance	0_W	0_W			15Dec24	15Dec24			
X49C15	Final Quantities Sent	0_W	0_W			29Mar25	29Mar25			




Project : 021727.00(0)

GREENBUSH, Boom Bridge #3587

								2018	2019	2020
Activity Name	Activity Description	Rem. Dur.	Orig. Dur.	actual start date	actual finish date	Early Start	Early Finish			
X49C17	All Bills Paid By Contractor	0_W	0_W			28Apr25	28Apr25			
								2018	2019	2020

Southport Bridge Schedule

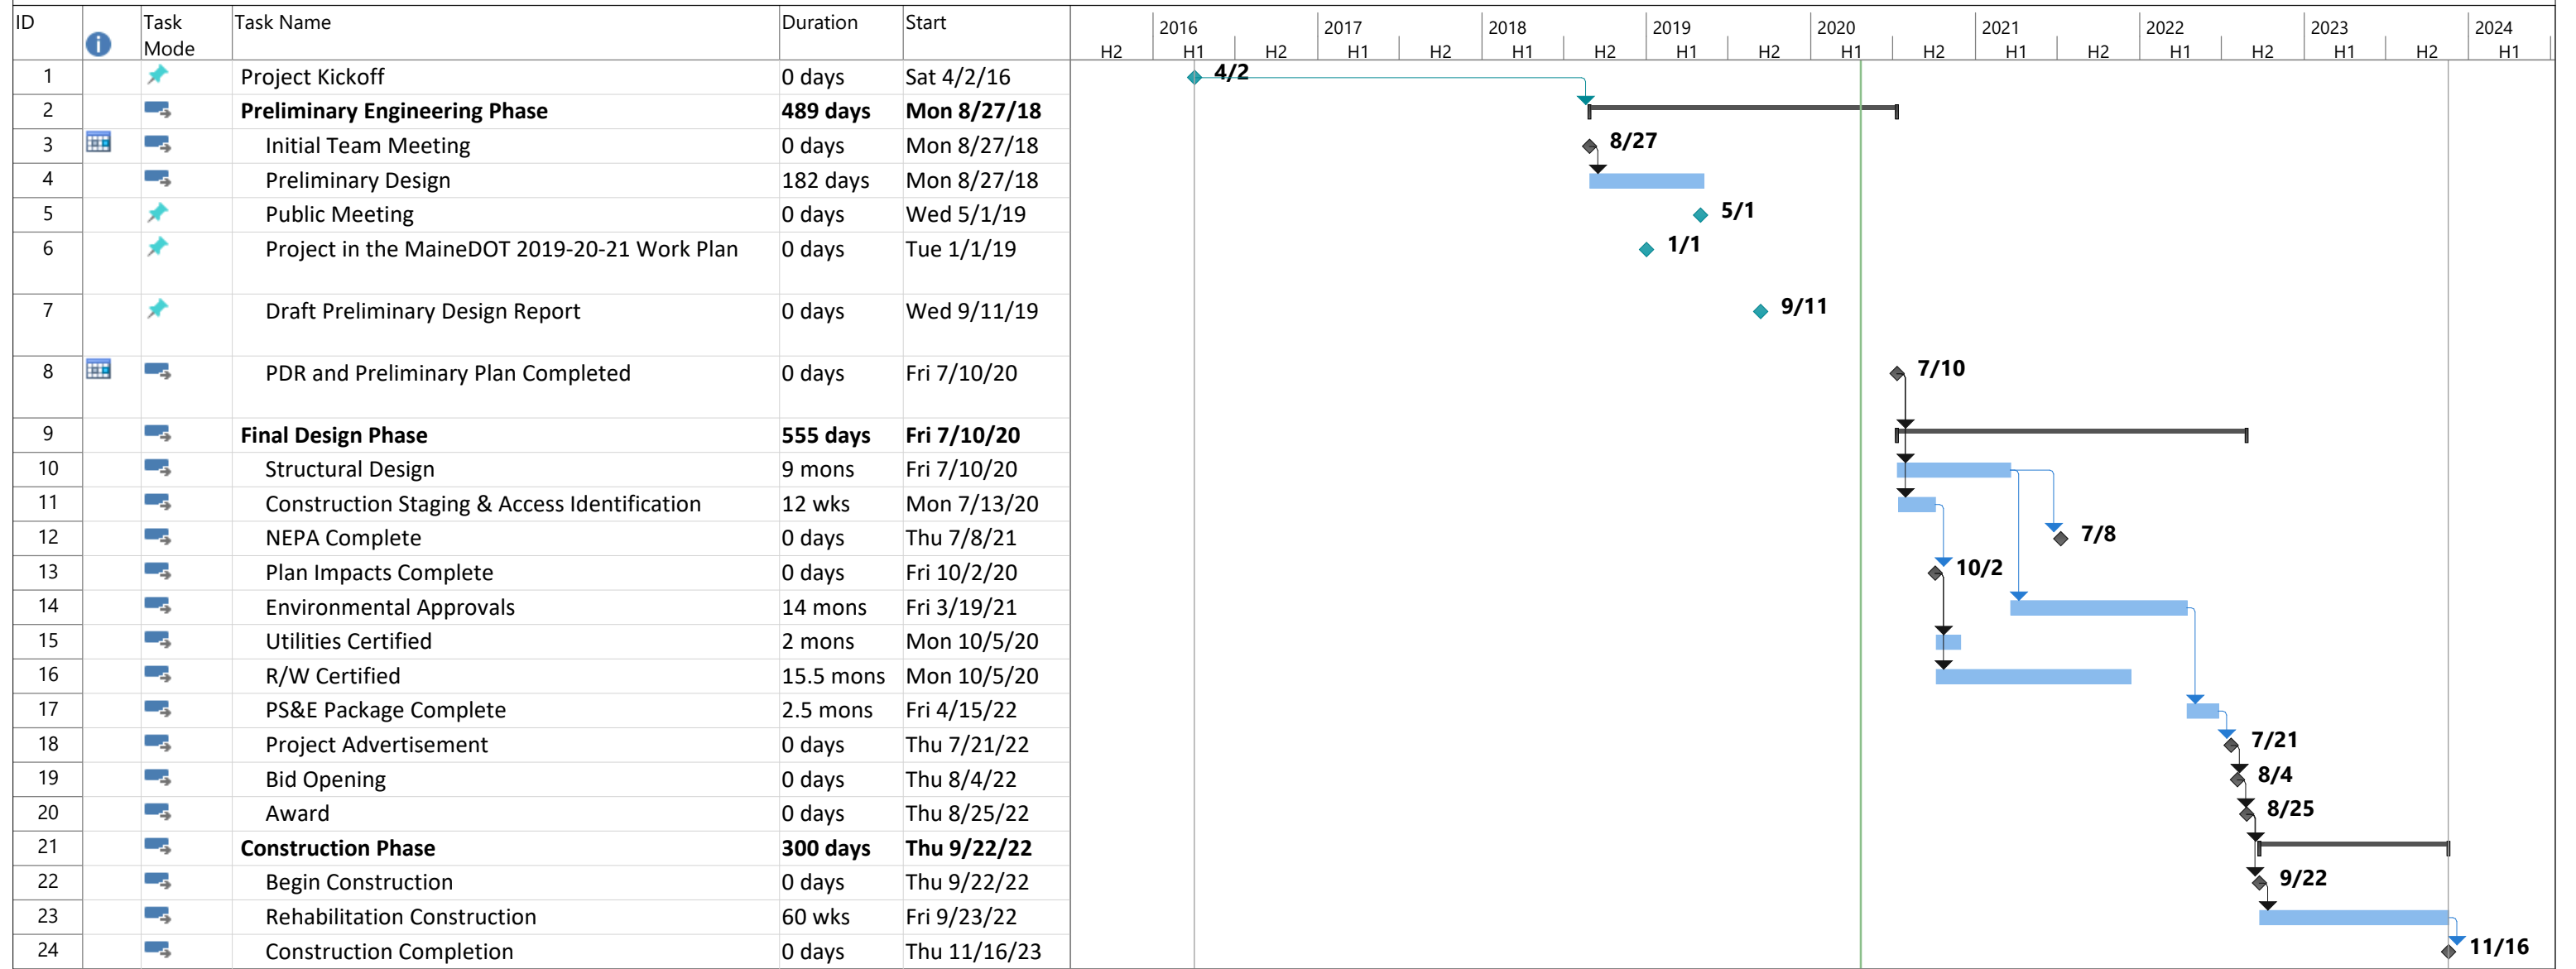

Project: Project Schedule
Date: Tue 4/21/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

Project : 020502.00(0)

MILo, Old Toll Bridge #2867

Activity Name	Activity Description	Rem. Dur.	Orig. Dur.	actual start date	actual finish date	Early Start	Early Finish	2020			2021			2022			
X01	PROJECT KICKOFF	0	0	27Dec13	27Dec13												
S45	Existing Conditions Report (survey, PORs & existing ROW)	0	90	30Dec13	02May14												
X07	INITIAL TEAM MEETING	0	0	21Mar14	21Mar14												
R38	Utilities Preliminary Coordination	0	20	24Mar14	18Apr14												
X09	PRELIMINARY PUBLIC MEETING	0	0	23Jul14	23Jul14												
D20	Preliminary Alignment Design	0	20	05May14	30May14												
D25	Preliminary Drainage Design	0	20	05May14	30May14												
G25	Preliminary Subsurface Exploration	0	30	24Mar14	02May14												
D30	Preliminary Structural Design	89	397	22Feb18			09Jul20										
D35	Preliminary Plan Development	56	56			10Jul20	25Sep20										
G45	Geotechnical Preliminary Design/Report	0	35	05May14	20Jun14												
X13	PDR/PRELIMINARY PLAN COMPLETE	0	0			25Sep20	25Sep20										
X15	FORMAL PUBLIC CONTACT	0	0			30Oct20	30Oct20										
G30	Final Subsurface Exploration	30	30			02Nov20	11Dec20										
D45	Final Highway Design/Detailing	93	93			02Nov20	10Mar21										
X21	PLAN IMPACTS COMPLETE	0	0			10Mar21	10Mar21										
X16	NEPA COMPLETE	0	0			16Apr21	16Apr21										
G50	Geotechnical Final Design/Report	25	25			11Mar21	14Apr21										
R53	R/W Final Mapping	110	110			11Mar21	11Aug21										
R32	Preparation of Titles	110	110			11Mar21	11Aug21										
R65	R/W Valuation	45	45			12Aug21	13Oct21										
R66	R/W Negotiation	30	30			14Oct21	24Nov21										
D50	Final Structural Design	200	200			26Feb21	02Dec21										
D55	Final Structural Plan Development	150	150			24Sep21	21Apr22										
D65	Final Estimate/Review	30	30			01Apr22	12May22										
R50	Utilities Final Coordination	40	40			11Mar21	05May21										
X23	UTILITIES CERTIFIED	0	0			05Jan22	05Jan22										
R74	R/W Condemnation/Acquisition	30	30			25Nov21	05Jan22										
R77	R/W Relocation Implementation	90	90			12Aug21	15Dec21										
E40	Environmental Evaluation	120	120			02Nov20	16Apr21										

Project : 020502.00(0)

MIL0, Old Toll Bridge #2867

								2020	2021	2022	
Activity Name	Activity Description	Rem. Dur.	Orig. Dur.	actual start date	actual finish date	Early Start	Early Finish				
X24	ENVIRONMENTAL COMPLETE PACKAGE (ECP)	0	0			16Apr21	16Apr21				
X25	R/W CERTIFIED	0	0			05Jan22	05Jan22				
D70	PS&E REVIEW	22	22			13May22	13Jun22				
X35	PS&E COMPLETE	0	0			13Jun22	13Jun22				
X39	PROJECT ADVERTISED	0	0			13Jul22	13Jul22				
X43	CONTRACT DATE	0	0			17Aug22	17Aug22				
X45	CONSTRUCTION BEGIN	0	0			26Apr23	26Apr23				
C30	Construction Administration	650	650			27Apr23	23Oct25				
X49	CONSTRUCTION COMPLETE	0	0			23Oct25	23Oct25				

Project : 024783.00(0)

BRIDGEWATER, WHITNEY BROOK BRIDGE #2942

								20	22	24	
Activity Name	Activity Description	Rem. Dur.	Orig. Dur.	actual start date	actual finish date	Early Start	early finish date	Gantt Chart Area			
X01	PROJECT KICKOFF	0	0			01May20	01May20				
X49C03	106 Memo	0_W	0_W			30Nov24	30Nov24				
S45	Preliminary Survey	75	75			11May20	21Aug20				
R35	Exisiting R/W & Ownership	15	15			02May20	16May20				
R36	Plot Exisiting R/W & Property Lines	15	15			22Aug20	05Sep20				
X04	EXISITING CONDITIONS PLAN	0	0			05Sep20	05Sep20				
X49C05	Buy America Cert	0_W	0_W			30Nov24	30Nov24				
X07	INITIAL TEAM MEETING	0	0			05Sep20	05Sep20				
X49C09	DBE Signoff	0_W	0_W			30Nov24	30Nov24				
X49C11	Final Acceptance	0_W	0_W			14Dec24	14Dec24				
X49C13	Final Records Submitted	0_W	0_W			14Mar25	14Mar25				
R38	Utilities Preliminary Coordination	20	20			07Sep20	02Oct20				
X09	PRELIMINARY PUBLIC MEETING	0	0			16Oct20	16Oct20				
X49C19	Agreement W/Final Quantities	0_W	0_W			27Apr25	27Apr25				
X49C21	Request for Final Payment Recieved	0_W	0_W			27Apr25	27Apr25				
X49C23	Other Need from Contractor	0_W	0_W			27Apr25	27Apr25				
XFINAL	Final Payment Made to Contractor	0_W	0_W			18May25	18May25				
X49C25	Commision Record/Final	0_W	0_W			17Jun25	17Jun25				
D20	Preliminary Alignment Design	15	15			07Sep20	25Sep20				
D25	Preliminary Drainage Design	25	25			07Sep20	09Oct20				
X49C27	Finals Folder Scanned	0_W	0_W			17Jul25	17Jul25				
G25	Preliminary Subsurface Exploration	30	30			07Sep20	16Oct20				
D30	Preliminary Structural Design	60	60			12Oct20	01Jan21				
X49C29	Final Plans Filed and Registered	0_W	0_W			02Jul26	02Jul26				
D35	Preliminary Plan Development	40	40			25Dec20	18Feb21				
X49C31	All Parcels Settled	0_W	0_W			02Jul26	02Jul26				
X49C99	Final Closed	0_W	0_W			09Jul26	09Jul26				
G45	Geotechnical Preliminary Design/Report	10	10			19Oct20	30Oct20				
X13	PDR/PRELIMINARY PLAN COMPLETE	0	0			18Mar21	18Mar21				
X15	FORMAL PUBLIC CONTACT	0	0			22Apr21	22Apr21				

Project : 024783.00(0)

BRIDGEWATER, WHITNEY BROOK BRIDGE #2942

								20	22	24
Activity Name	Activity Description	Rem. Dur.	Orig. Dur.	actual start date	actual finish date	Early Start	early finish date			
G30	Final Subsurface Exploration	30	30			23Apr21	03Jun21			
D45	Final Highway Design/Detailing	75	75			23Apr21	05Aug21			
X21	PLAN IMPACTS COMPLETE	0	0			05Aug21	05Aug21			
E40	Environmental coordination	100	100			23Apr21	09Sep21			
X16	NEPA COMPLETE	0	0			09Sep21	09Sep21			
G50	Geotechnical Final Design/Report	15	15			06Aug21	26Aug21			
R53	R/W Mapping	125	125			06Aug21	27Jan22			
R32	Preraration of Titles	90	90			10Sep21	13Jan22			
R32.1	Verification of Titles	30	30			28Jan22	26Feb22			
R53.1	Final R/W Maps	15	15			27Feb22	13Mar22			
R65	R/W Valuation	20	20			14Mar22	08Apr22			
R66	R/W Negotiation	20	20			11Apr22	06May22			
D50	Final Structural Design	70	70			06Aug21	11Nov21			
D55	Final Structural Plan Development	70	70			14Oct21	19Jan22			
D65	Final Estimate/Review	15	15			20Jan22	09Feb22			
R50	Utilities Final Coordination	40	40			06Aug21	30Sep21			
X23	UTILITIES CERTIFIED	0	0			30Sep21	30Sep21			
R74	R/W Condemnation/Acquisition	30	30			09May22	17Jun22			
X24	ENVIRONMENTAL COMPLETE PACKAGE(ECR)	0	0			09Sep21	09Sep21			
X25	R/W CERTIFIED	0	0			17Jun22	17Jun22			
D70	PS&E REVIEW	20	20			23May22	17Jun22			
X35	PS&E COMPLETE	0	0			17Jun22	17Jun22			
X39	PROJECT ADVERTISED	0	0			13Jul22	13Jul22			
X43	CONTRACT DATE	0	0			17Aug22	17Aug22			
X45	CONSTRUCTION BEGIN	0	0			28Jun23	28Jun23			
C30	Construction Administration	350	350			29Jun23	31Oct24			
X49	CONSTRUCTION COMPLETE	0	0			31Oct24	31Oct24			
X49C01	Physical Work Complete Letter Sent	0_W	0_W			31Oct24	31Oct24			
X49C07	Material Certs	0_W	0_W			30Nov24	30Nov24			
X49C15	Final Quantities Sent	0_W	0_W			28Mar25	28Mar25			

Project : 024783.00(0)

BRIDGEWATER, WHITNEY BROOK BRIDGE #2942

Activity Name	Activity Description	Rem. Dur.	Orig. Dur.	actual start date	actual finish date	Early Start	early finish date	20	22	24
X49C17	All Bills Paid By Contractor	0_W	0_W			27Apr25	27Apr25			
▼										
ProjectView										
								20	22	24
