


ID	Task	Task Name	Duration	Start	Finish	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032
0		Sanford RAISE Grant	147.05 mons?	Wed 7/17/19	Fri 10/18/30														
1		Planning	22.2 mons	Wed 7/17/19	Mon 3/29/21														
2		Planning Partnership Initiative	22.2 mons	Wed 7/17/19	Mon 3/29/21														
3		Roadway Safety Audit	162 days	Wed 7/17/19	Thu 2/27/20														
4		Public Hearing #1	0 mons	Thu 4/16/20	Thu 4/16/20														
5		Public Hearing #2	0 mons	Thu 7/9/20	Thu 7/9/20														
6		Feasibility Study	8.8 mons	Mon 3/30/20	Mon 11/30/20														
7		Preliminary Design	18.75 mons?	Tue 3/30/21	Thu 9/1/22														
8		Initial Team Meeting	0 mons	Thu 6/3/21	Thu 6/3/21														
9		Preliminary Public Meeting	0 mons	Wed 12/15/21	Wed 12/15/21														
10		Prelim. Alignment Complete	0 mons	Sat 12/25/21	Sat 12/25/21														
11		Draft PDR Distribution	0 mons	Fri 3/25/22	Fri 3/25/22														
12		Preliminary Plan Complete	0 mons	Thu 9/1/22	Thu 9/1/22														
13		Local Review Process	12.35 mons?	Wed 6/1/22	Thu 5/11/23														
14		NEPA Process	12.35 mons?	Wed 6/1/22	Thu 5/11/23														
15		Final Design	43.3 mons?	Fri 9/2/22	Thu 12/25/25														
16		Formal Public Contact	0 mons	Mon 10/31/22	Mon 10/31/22														
17		Section 7 Sign-Off	0 mons	Thu 5/11/23	Thu 5/11/23														
18		Plan Impacts Complete	0 mons	Wed 11/1/23	Wed 11/1/23														
19		Final ROW Mapping	0 mons	Thu 8/1/24	Thu 8/1/24														
20		ROW Appraisals Complete	0 mons	Sun 6/1/25	Sun 6/1/25														
21		Utilities Certified	0 mons	Fri 6/13/25	Fri 6/13/25														
22		Environmental Approvals Complete	0 mons	Fri 6/13/25	Fri 6/13/25														
23		ROW Negotiations	0 mons	Mon 9/1/25	Mon 9/1/25														
24		Right of Way Certified	26.85 mons?	Wed 11/1/23	Wed 11/19/25														
25		PS&E Complete	0 mons	Thu 12/4/25	Thu 12/4/25														
26		Advertise for Construction	0 mons	Thu 12/25/25	Thu 12/25/25														
27		Construction	61.8 mons	Sat 1/24/26	Fri 10/18/30														
28		Contract Award	0 mons	Sat 1/24/26	Sat 1/24/26														
29		Begin Construction	0 mons	Tue 2/24/26	Tue 2/24/26														
30		Project Complete	0 days	Fri 10/18/30	Fri 10/18/30														

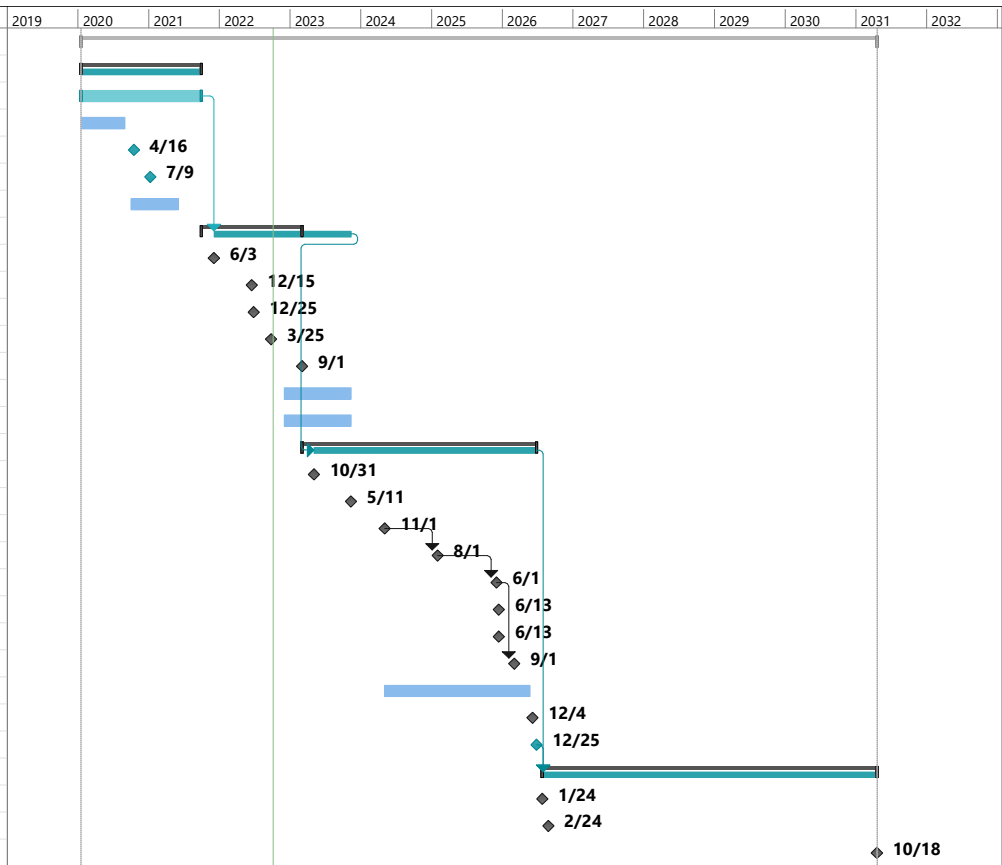

Project: Sanford RAISE Grant Date: Tue 4/5/22	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Milestone		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			
