


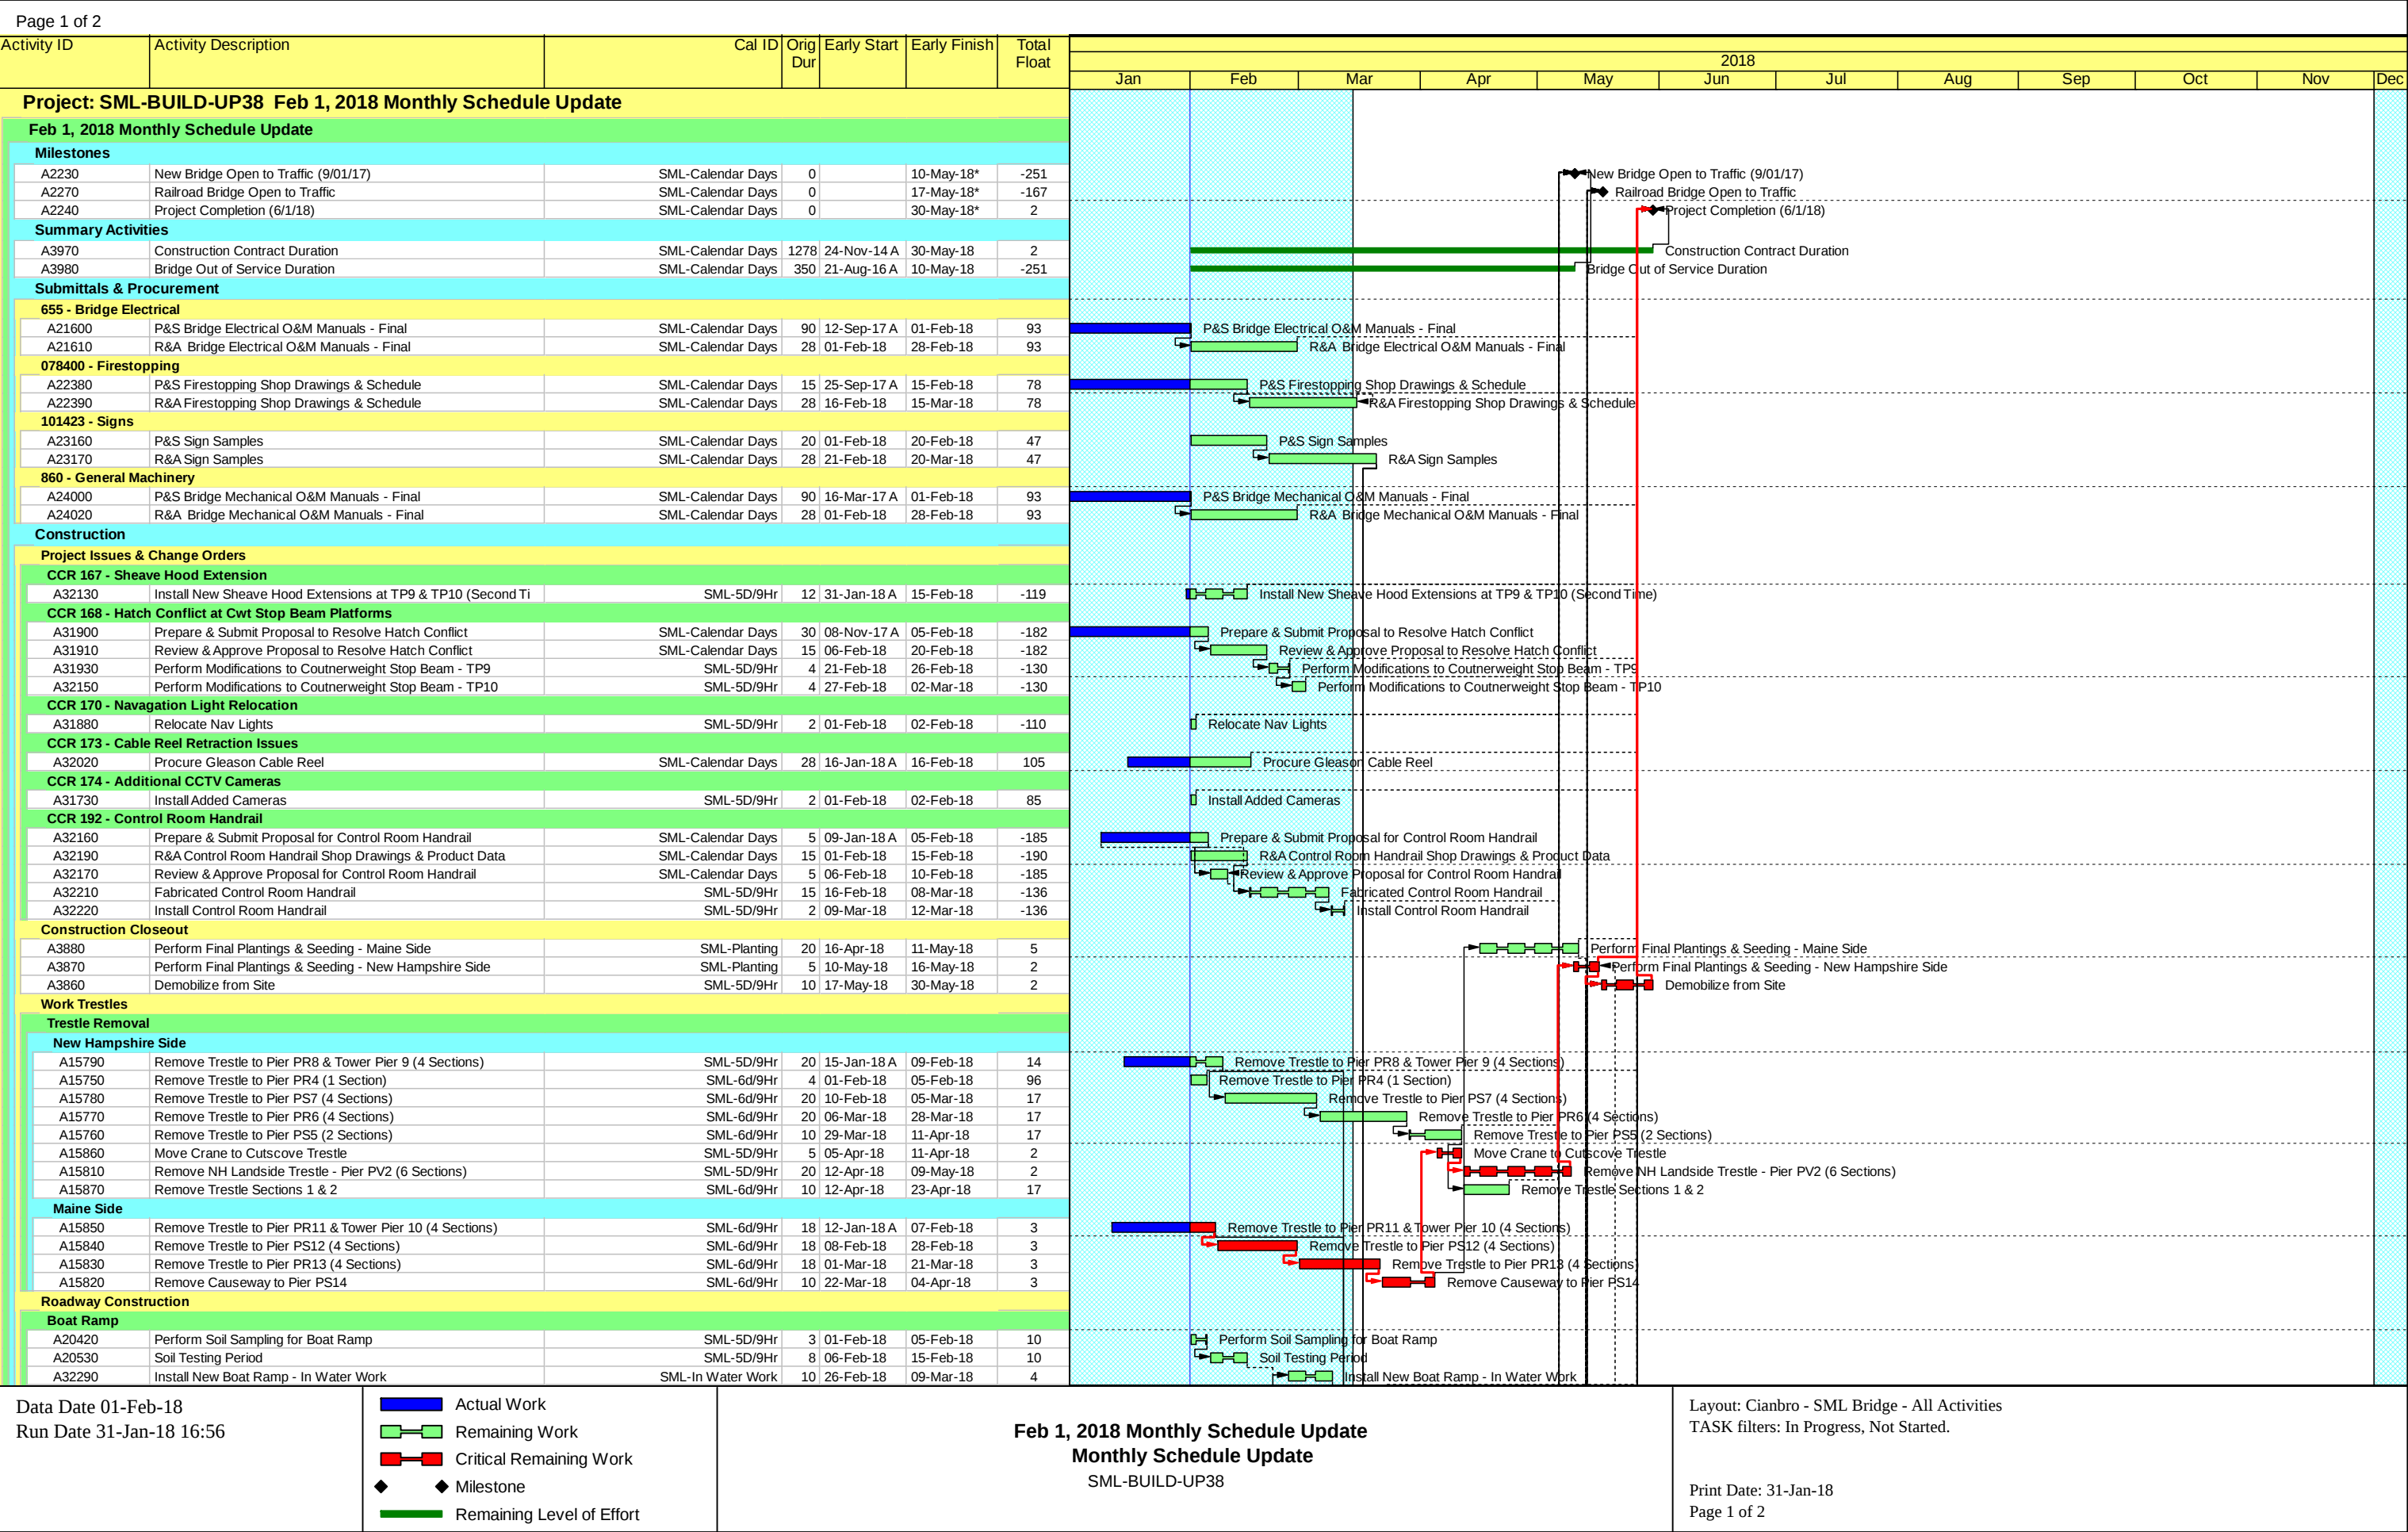

Activity ID	Activity Description	Cal ID	Orig Dur	Early Start	Early Finish	Total Float	2018																
							Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec					
A19300	Install New Boat Ramp	SML-5D/9Hr	10	12-Mar-18	23-Mar-18	50																	
Railroad Construction																							
New Hampshire Side																							
A15360	Construct New Railroad Approaches to Abutment 1	SML-Weather Restriction	45	16-Mar-18	17-May-18	-54																	
Maine Side																							
A15380	Construct New Railroad Approaches to Abutment 2	SML-Weather Restriction	25	20-Nov-17 A	06-Apr-18	-54																	
Bridge Approaches																							
Sub Structure																							
New Hampshire Side																							
Tower Pier 9																							
Tower Finishes																							
Mechanical Room																							
A16210	Install Mechanical Room Finishes at Pier TP9	SML-5D/9Hr	20	21-Mar-18	17-Apr-18	33																	
Electrical Room																							
A16220	Install Electrical Room Finishes at Pier TP9	SML-5D/9Hr	20	21-Mar-18	17-Apr-18	33																	
Railroad																							
A16190	Install Fixed Track & Expansion Joint at Pier TP9	SML-5D/9Hr	5	25-Jan-18 A	06-Feb-18	-112																	
Pier Epoxy																							
A15980	Apply Epoxy to Top of Pier TP9	SML-Weather Restriction	20	16-Mar-18	12-Apr-18	36																	
Bird Control Devices																							
A24380	Install Bird Control Devices at TP9	SML-5D/9Hr	5	01-Feb-18	07-Feb-18	82																	
Point & Patch																							
A32270	Point & Patch Tower Pier TP9	SML-Weather Restriction	20	16-Mar-18	12-Apr-18	-114																	
Maine Side																							
Tower Pier 10																							
Tower Finishes																							
Mechanical Room																							
A16230	Install Mechanical Room Finishes at Pier TP10	SML-5D/9Hr	20	21-Mar-18	17-Apr-18	33																	
Electrical Room																							
A16240	Install Electrical Room Finishes at Pier TP10	SML-5D/9Hr	20	21-Mar-18	17-Apr-18	33																	
Joints																							
A10870	Install Finger Joints (2ea) at Pier TP10 - Railroad	SML-5D/9Hr	8	01-Feb-18	12-Feb-18	-81																	
Railroad																							
A16200	Install Fixed Track & Expansion Joint at Pier TP10	SML-5D/9Hr	5	25-Jan-18 A	06-Feb-18	-112																	
Pier Epoxy																							
A15990	Apply Epoxy to Top of Pier TP10	SML-Weather Restriction	20	16-Mar-18	12-Apr-18	36																	
Bird Control Devices																							
A24390	Install Bird Control Devices at TP10	SML-5D/9Hr	5	01-Feb-18	07-Feb-18	82																	
Point & Patch																							
A32280	Point & Patch Tower Pier TP10	SML-Weather Restriction	20	13-Apr-18	10-May-18	-114																	
Super Structure																							
New Hampshire Side																							
Railroad Bridge Deck Work																							
Railroad Finishes																							
A15660	Apply Deckguard on RR Spans from Abut 1 to Tower 9	SML-Weather Restriction	15	16-Mar-18	05-Apr-18	-54																	
A32250	Point & Patch NH Approach Railroad Approach Spans	SML-Weather Restriction	10	16-Mar-18	29-Mar-18	-29																	
A2160	Install Ballast, Ties & Rails From Abut 1 to Tower 9	SML-5D/9Hr	30	06-Apr-18	17-May-18	-119																	
Roadway Bridge Deck Work																							
Roadway Finishes																							
A32080	Apply Pavement Markings NH Approach - Thermo	SML-Weather Restriction	2	16-Mar-18	19-Mar-18	54																	
A32230	Point & Patch NH Approach Vehicular Approach Spans	SML-Weather Restriction	15	16-Mar-18	05-Apr-18	-104																	
A32240	Apply Curb Protective Coating NH Approach Vehicular Approach	SML-Weather Restriction	5	16-Mar-18	22-Mar-18	-79																	
Maine Side																							
Railroad Bridge Deck Work																							
Railroad Finishes																							
A15670	Apply Deckguard on RR Spans from Abut 2 to Tower 10	SML-Weather Restriction	15	16-Mar-18	05-Apr-18	-54																	
A32260	Point & Patch ME Approach Railroad Approach Spans	SML-Weather Restriction	10	30-Mar-18	12-Apr-18	-29																	
A2670	Install Ballast, Ties & Rails from Abut 2 to Tower 10	SML-5D/9Hr	30	06-Apr-18	17-May-18	-119																	
Roadway Bridge Deck Work																							
Roadway Finishes																							
A2740	Apply Curb Protective Coating ME Approach Vehicular Approach	SML-Weather Restriction	5	16-Mar-18	22-Mar-18	-79																	
A2730	Point & Patch ME Approach Vehicular Approach Spans	SML-Weather Restriction	15	06-Apr-18	26-Apr-18	-104																	
Movable Bridge																							
Lift Span Testing and Acceptance																							
A13930	Perform Operating Rope Tension Adjustments	SML-5D/9Hr	2	31-Jan-18 A	01-Feb-18	-118																	
A13940	Replace Reducer Seal - TP9	SML-5D/9Hr	1	01-Feb-18	01-Feb-18	-118																	
A13950	Adjust Takeup Nuts - TP9 & TP10	SML-5D/9Hr	4	02-Feb-18	07-Feb-18	-118																	
A14030	Touchup Paint Lifting Girders - TP9 & TP10	SML-Weather Restriction	5	16-Mar-18	22-Mar-18	-79																	
Bridge Utilities																							
Water Service																							
A16170	Run Water Service from NH Side - On Bridge	SML-5D/9Hr	15	18-Dec-17 A	21-Feb-18	72																	
Demolition of Existing Bridge																							
New Hampsire Side																							
Existing Barge Wharf																							
A5240	Remove Remaining Existing Barge Wharf Sections	SML-5D/9Hr	25	22-Jan-18 A	23-Feb-18	4																	
