


Bill of Materials

PANEL	N. TOP BEARING BARS	LENGTH	N. BOTTOM BEARING BARS	LENGTH	N. TOP CROSS BARS	LENGTH	N. BOTTOM CROSS BARS	LENGTH	NUMBER OF BARS	LENGTH	NUMBER OF BARS	LENGTH
E1-E	36	20-7 1/2	36	20-7 1/2	16	4-7 1/2	24	4-3 3/4	18	23-10 1/2	2	20-7 1/2
E2-E	36	20-7 1/2	36	20-7 1/2	25-8	4-1	72	4-1	48	23-10 1/2	-	-
E3-E	36	20-7 1/2	36	20-7 1/2	34	4-1	24	4-0 3/4	16	23-10 1/2	2	20-7 1/2
F1-F	36	13-8 3/4	36	13-8 3/4	56	4-7 1/2	16	4-3 3/4	18	15-11	2	13-8 3/4
F2-F	36	13-8 3/4	36	13-8 3/4	16-8	4-1	48	4-1	48	15-11	-	-
F3-F	36	13-8 3/4	36	13-8 3/4	36	4-1 1/2	16	4-0 3/4	16	15-11	2	13-8 3/4

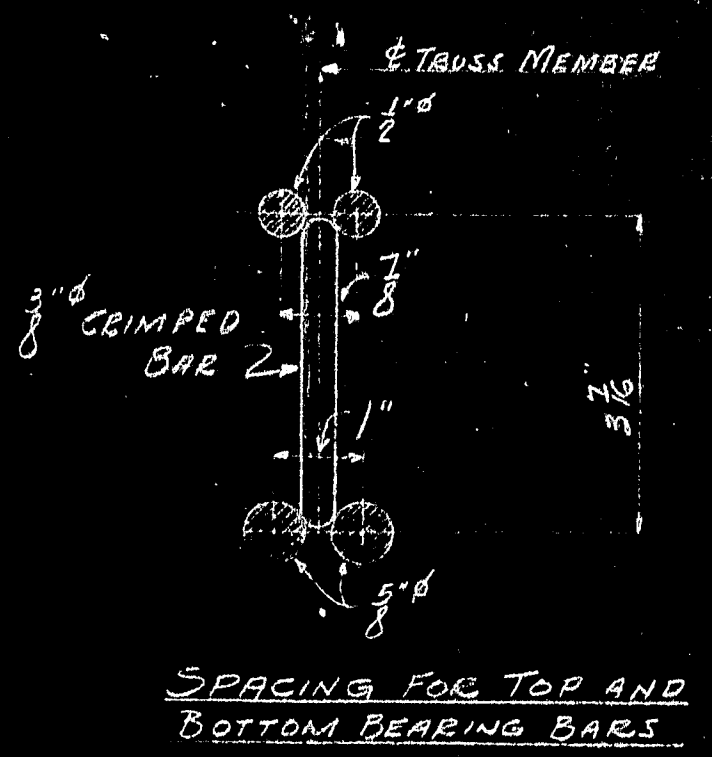

Notes:
FOR FORM 12 SPACING SEE DWG. 3031-5
FOR ALL OTHER NOTES SEE DWG. 3031-1

CUSTOMER THE PHOENIX BRIDGE CO. PHOENIXVILLE, PENNA.		RELiance STEEL PRODUCTS COMPANY	
PROJECT RANKIN, (PITTSBURGH DISTRICT) PA. BRIDGE		DEPARTMENT	
LOCATION DEER ISLE - BEDFORD BRIDGE, HANCOCK COUNTY, MD.		PROJECT PWA PROJECT ME 1010 D	
CUSTOMER ORDER NO.	REFERENCE	DRAWN L.M. 2-20-38	APPROVED BY G.M.H. 5-23-38
DATE	DATE	DWG. NO. 3031-4	CONTRACT NO. G 3345

