

2025 Southern ADA

Mars Hill

CR14766

Main Street Mid Block (Park)

North End

- Remove and Reset 16 LF Granite Curb
- ADA plates 4'x2'
- 403.209 and Regrade sidewalk 20'x4'




CR14767

Main Street Mid Block (Park) South

End


- Remove and Reset 16 LF Granite Curb
- ADA plates 4'x2'
- 403.209 and Regrade sidewalk 20'x4'

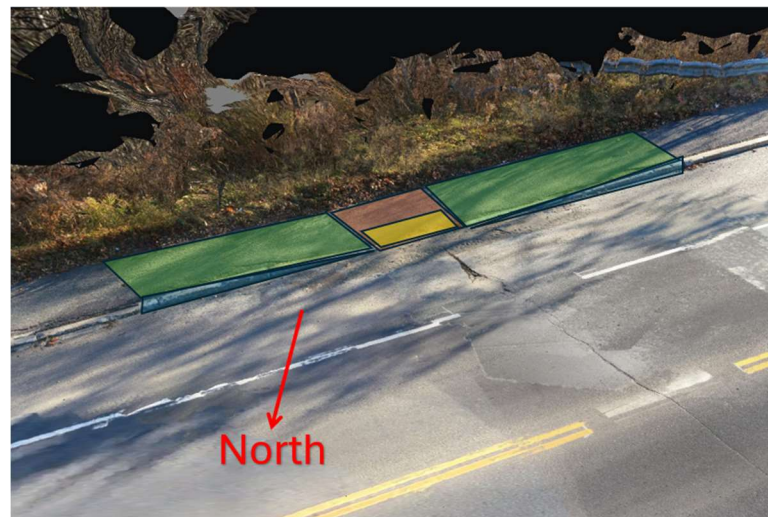

CR04485

Corner of Pleasant and Bridge
Street


- Reset 16LF of Granite Curb
- ADA Plates 4'x2'
- 403.209 and Regrade 20'x4'

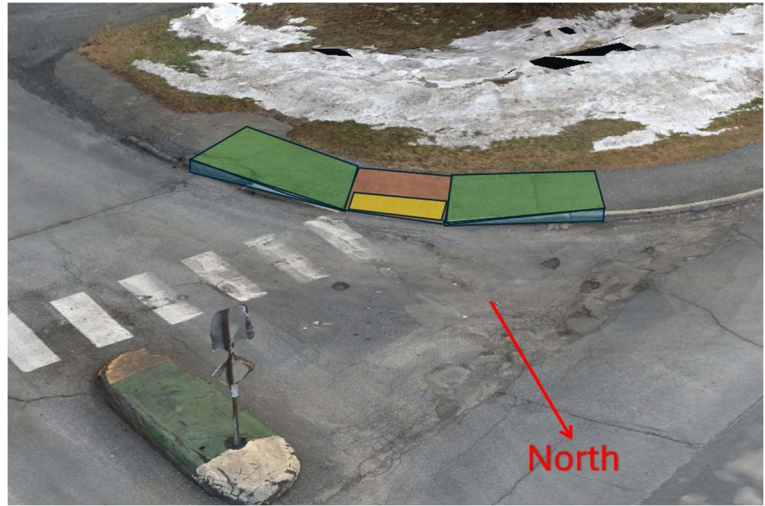

CR14614

Between Church and Pleasant
Streets

- Remove two sections of Granite Curb
- 8' Curb Type III
- ADA Plates 5'x2'
- 403.209 and Regrade 20'x4'

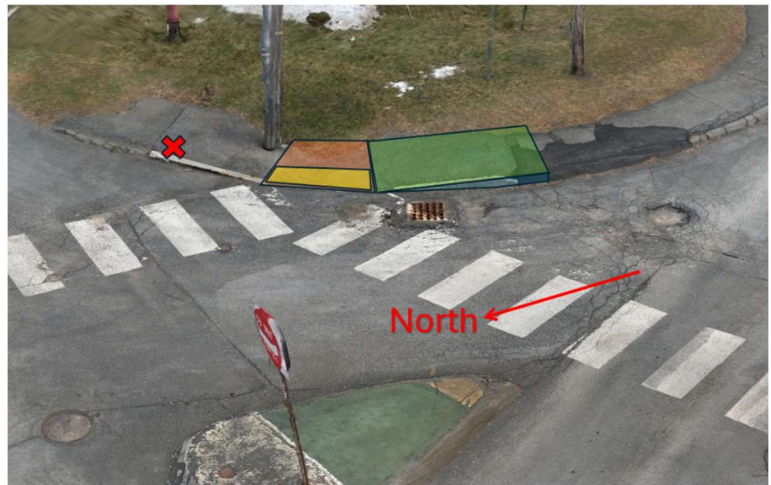

CR14615

Corner of Church and Fort Street


- Remove and Reset 8' of Granite Curb
- ADA Plates 4'x2'
- 403.209 and Regrade 12'x4'



CR04489

Fort Street Mid Block (Gilman ST)
East Side


- Remove and Reset 24' of Granite Curbing (Swap the 4' and 8' Pieces)
- Ada plates 5'x2'
- 403.209 and Regrade 30'x4'

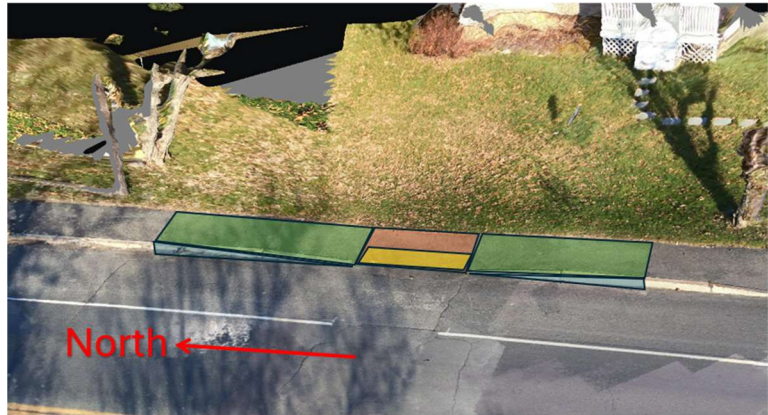

CR04490


Fort Street Mid Block (Gilman ST)
West Side

- Take Granite curb from CR-14614 and close up opening
- Reset 24 LF of Granite Curbing
- ADA Plates 5'x2'
- 403.209 and Regrade 32'x4'
- Loam and seed

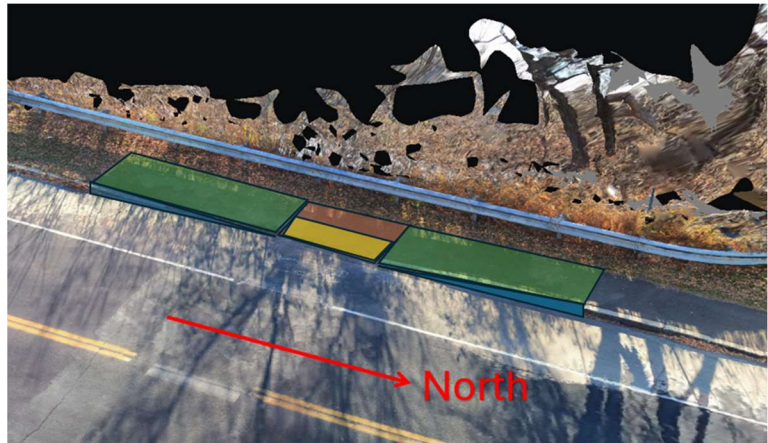


CR04491 Boynton and Fort Street
North

- Remove 12' existing granite curb and reset 8' of it.
- ADA plates 4'x2'
- 403.209 and Regrade sidewalk 12'x4'

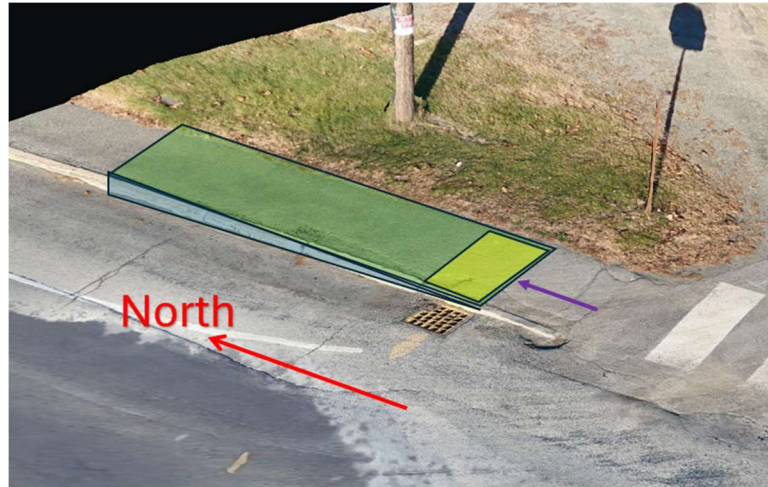


CR04492
Boynton and Fort Street South

- Remove 12' of Existing Granite Curb cut pieces to put back 8'
- ADA Plates 4'x2'
- 403.209 and Regrade sidewalk 12'x4'

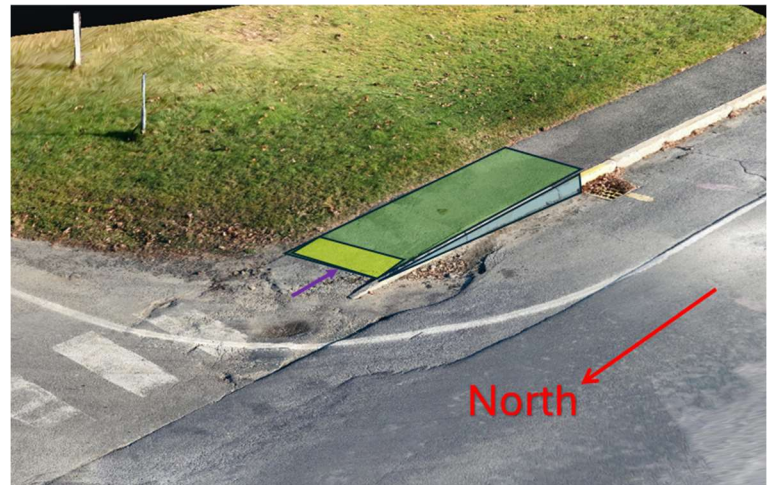

CR15045
Mid Block at School (East Side)


- Remove and Reset 2-8' and 1-6' sections of existing granite curb swap the 8' and 6' sections
- ADA Plates 4'x2'
- 403.209 and Regrade sidewalk 26'x4'

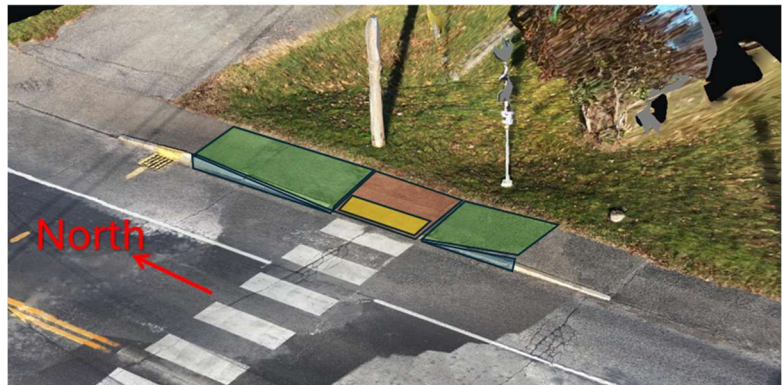

CR15046

Mid Block at School (West Side)

- Remove and Reset 2-8' and 1-6' sections of existing granite curb swap the 8' and 6' sections
- ADA Plates 4'x2'
- 403.209 and Regrade sidewalk 26'x4'

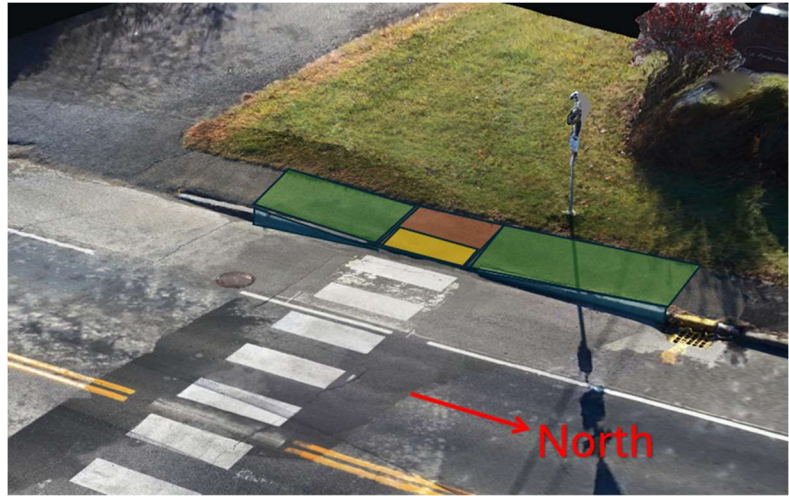


Construction Notes

St. Agatha

CR11016

(North End Cleveland Road)

- 8' Type III Curb Mold 3
- ADA Plate 4'x2'
- 403.209 HMA and Regrade sidewalk 12'x4'
- Adjust Manhole

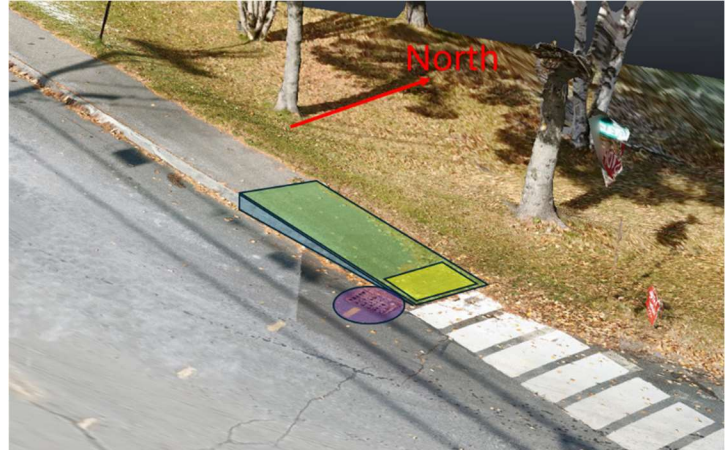

Caribou

CR08987

(Glenn Street North East Corner)

- 16' Type III Curb Mold 3
- ADA Plate 8'x2' Radius or Cut to a Radius
- 403.209 HMA and regrade sidewalk 26'x4'



CR18029

(Glenn Street North West Corner)

- 8' Curb Type III Mold 3
- ADA Plate 4'x2' (Move back up sidewalk 2' from existing location)
- 403.209 HMA and regrade sidewalk 10'x4'



CR17397

(Mid Block at Hannaford's)


- Remove middle curb
- 8' Type III Curb
- ADA Plates 6'x2'
- 403.209 and regrade sidewalk 14'x4'



CR17398

(Mid Block at Fire station)


- 8' Type III Curb
- ADA Plate 6'x2'
- 403.209 and regrade sidewalk 14'x4'

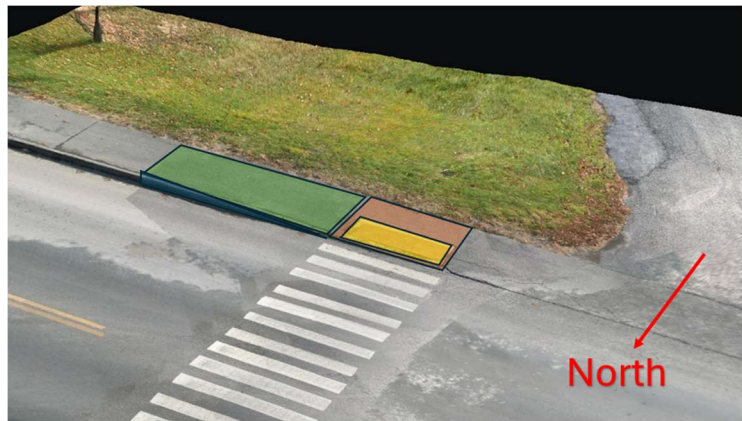

CR14393

Mid Block Hatch Drive West side
(Dollar General)


- 8' Type III Curb
- 8' Type III Curb (Back)
- Remove Concrete sidewalk
- ADA plates 6'x2'
- 403.209 and Regrade Sidewalk 10'x5'

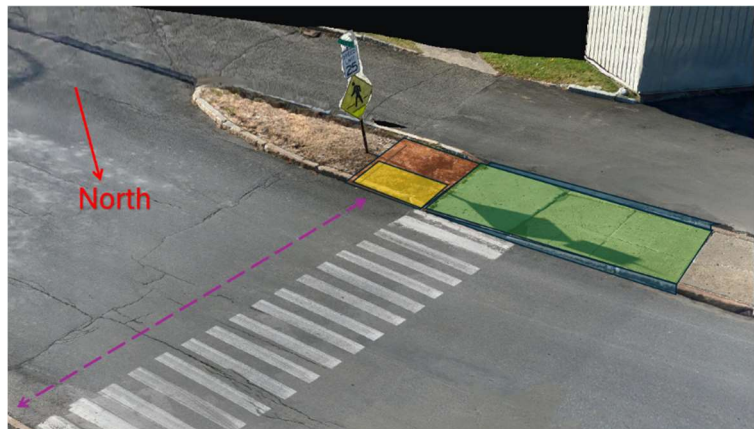

CR10960

Mid Block Hatch Drive East Side
(Movie Theater)

- Remove Granite Curbing,
- New 8' Granite Tip Downs x2
- Remove Concrete to Crack
- ADA Plates 6'x4'
- Extend sidewalk south
- 403.209 and Regrade 12'x5'

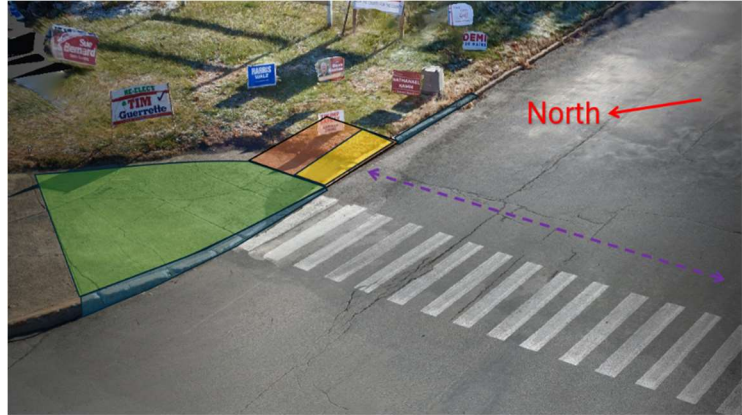

CR10958

North West Corner of Prospect Street
and Sweden St (Methodist Church)

- New 1- 8' Granite Radius Tip
Down 1- 8'Radius Granite
- 8' Type III Curb
- ADA Plate 4'x2'
- 403.209 and Regrade 28'x4'



CR10957

North East Corner of Prospect Street
and Sweden ST

- 1 8' Granite tip down
- ADA plates 4' x 2'
- 403.209 and Regrade 10'x 4'




St. Agatha, Caribou, Presque Isle
28882.00
Routes, 161 B, 161 BS, 162, Skyway St.
February 26, 2025

CR17374

Mid Block Sweden Street (Ruska Coffee)


- Moving East to other side of utility poles
- 4 sections of 8' Tip down Granite curb
- ADA Plates 6'x2'
- Remove entire concrete island
- 403.209 and Regrade 10'x30'

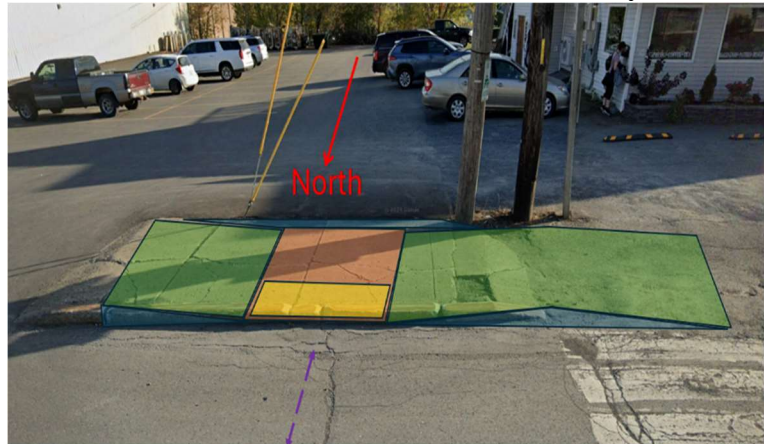

CR17373

Mid Block Sweden Street (Methodist Church)


- Move crossing east, line up with walkway from church
- Type III Curb 16'
- ADA Plates 6'x2'
- 403.209 and Regrade 22'x4' Plus 8'x4' for church walkway

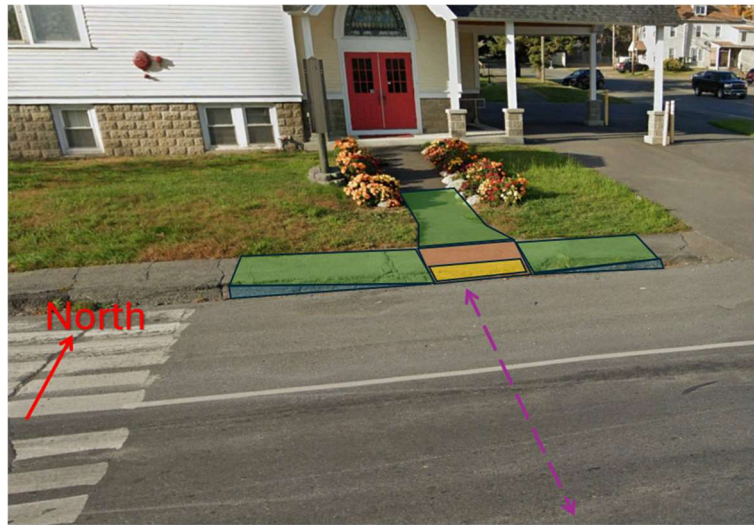

CR17375


Mid Block Sweden ST South Side (Assembly of God)

- Move Crossing to South East Corner of Summer St and Sweden Street
- 8' Type III Curb
- ADA Plates 4x2 and 4x2
- 403.209 and Regrade 12'x4'

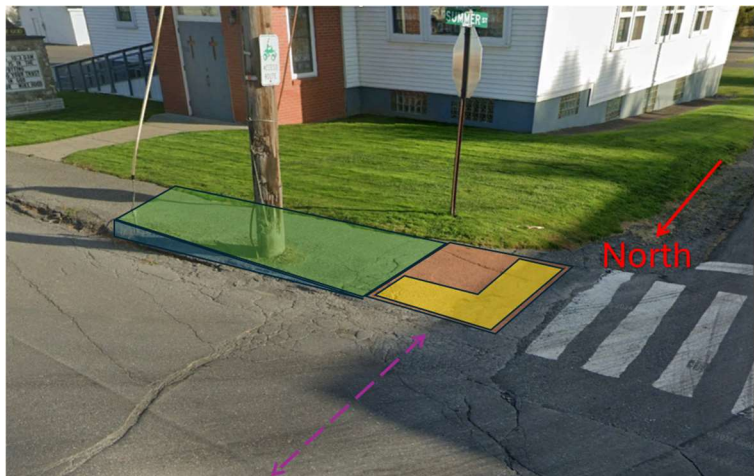


CR17372 Mid Block Sweden ST
North Side (Renos)

- Move Crossing West to line up with CR17375
- ADA Plates 6'x4'
- Type III Curb 20' Back Curb and 8' Front Curb
- 403.209 and Regrade 20'x4'

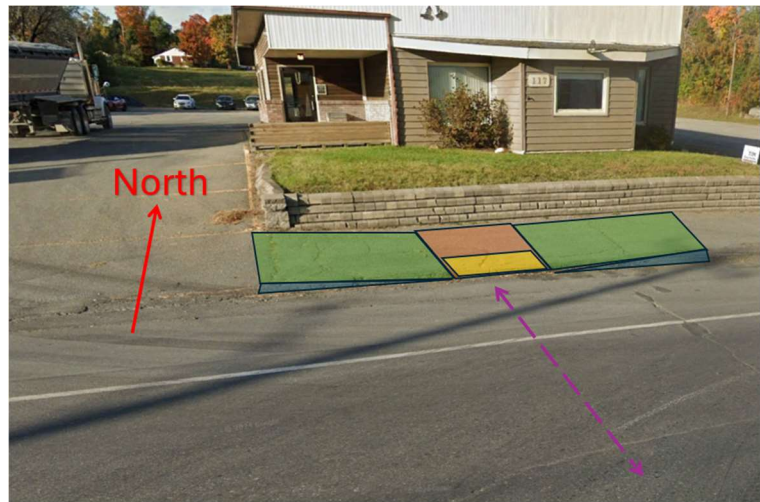


CR17376
Mid Block Sweden ST South Side
(Court House)

- Move Crossing East to other side of utility poles approximately 25'
- Type III curb 16'
- ADA Plates 6'x2'
- 403.209 and Regrade 21'x4'

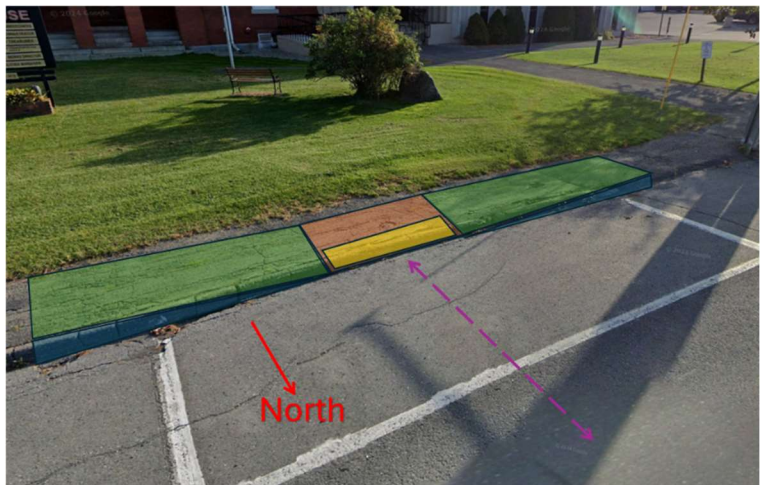

CR17371
Mid Block Sweden ST North Side


- Move Crossing East to line up with CR 17376
- Type III curb 16'
- ADA Plates 6'x2'
- 403.209 and Regrade 21'x4'

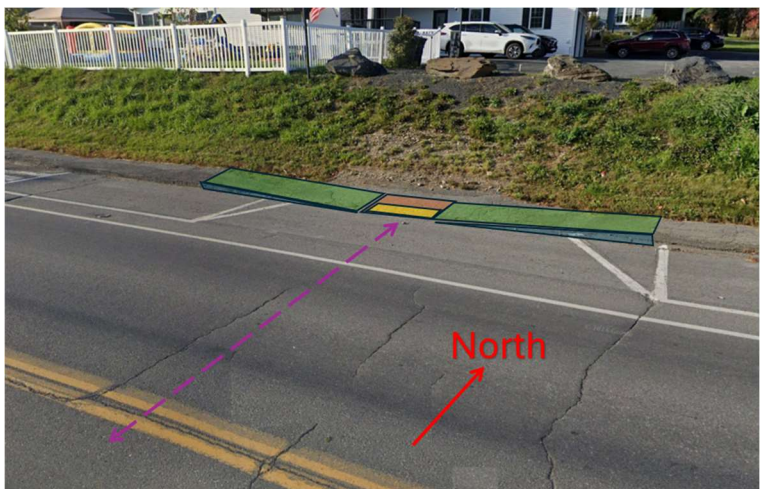

CR10973

Raymond ST and Sweden ST South
Side

- Type III Curb 8'
- ADA Plate 4'x2'
- 403.209 and Regrade 12'x4'

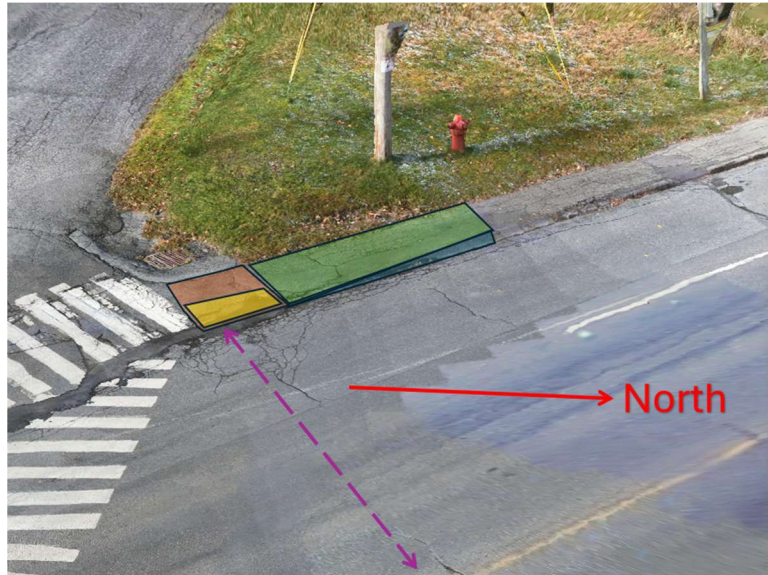

CR17369

Raymond ST and Sweden ST
North Side

- Move Crossing West to be perpendicular with CR 10973
- Construct Sidewalk 70'
- Type III curb 70'
- ADA Plates 4'x2'
- 403.209 70'x4'




Presque Isle

No CR #

Skyway ST. MidBlock North East
Corner

- Remove Concrete Block
- ADA Plate 5'x 2'
- 403.209 and Regrade 5'x4'
- Loam and Seed Edges

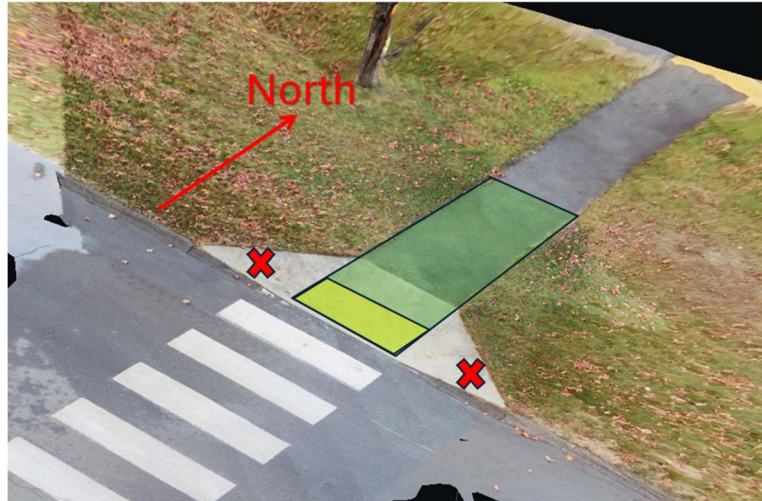

No CR#

Skyway ST. MidBlock South East
Corner


- Curb Type III 16 LF
- ADA Plates 6'x2'
- 403.209 and Regrade 22'x6'



No CR#

Skyway ST. MidBlock North West
Corner

- Remove Concrete Block
- ADA Plate 5'x 2'
- 403.209 and Regrade 5'x4'
- Loam and Seed Edges

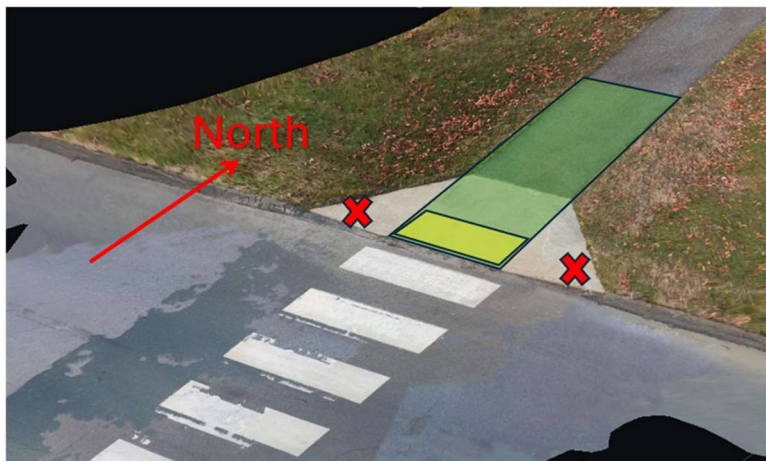

No CR#

Skyway ST. MidBlock South West
Corner

- Curb Type III 16 LF
- ADA Plates 6'x2'
- 403.209 and Regrade 22'x6'

