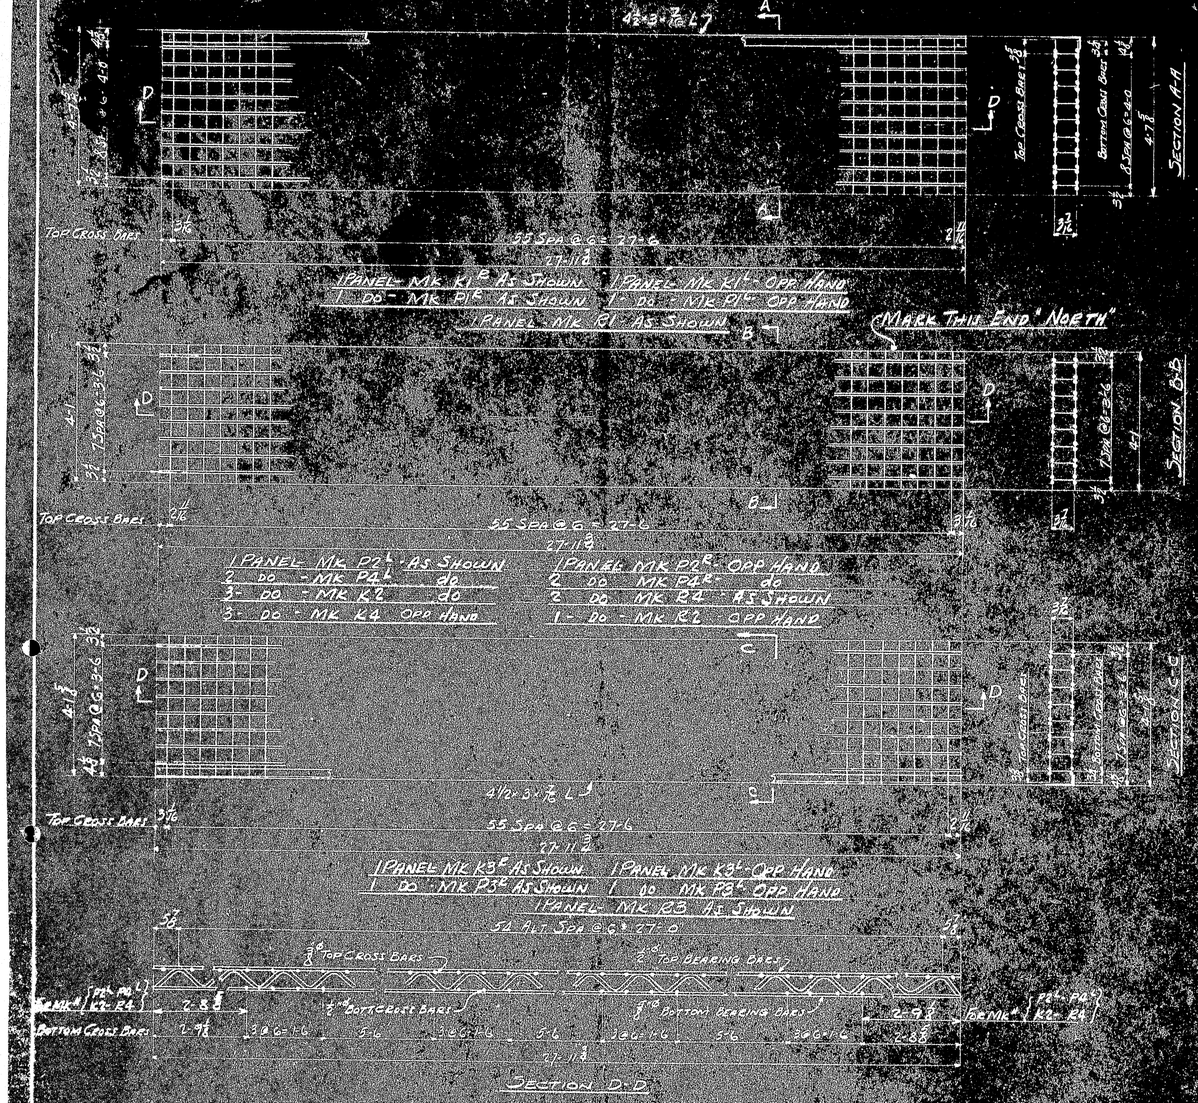

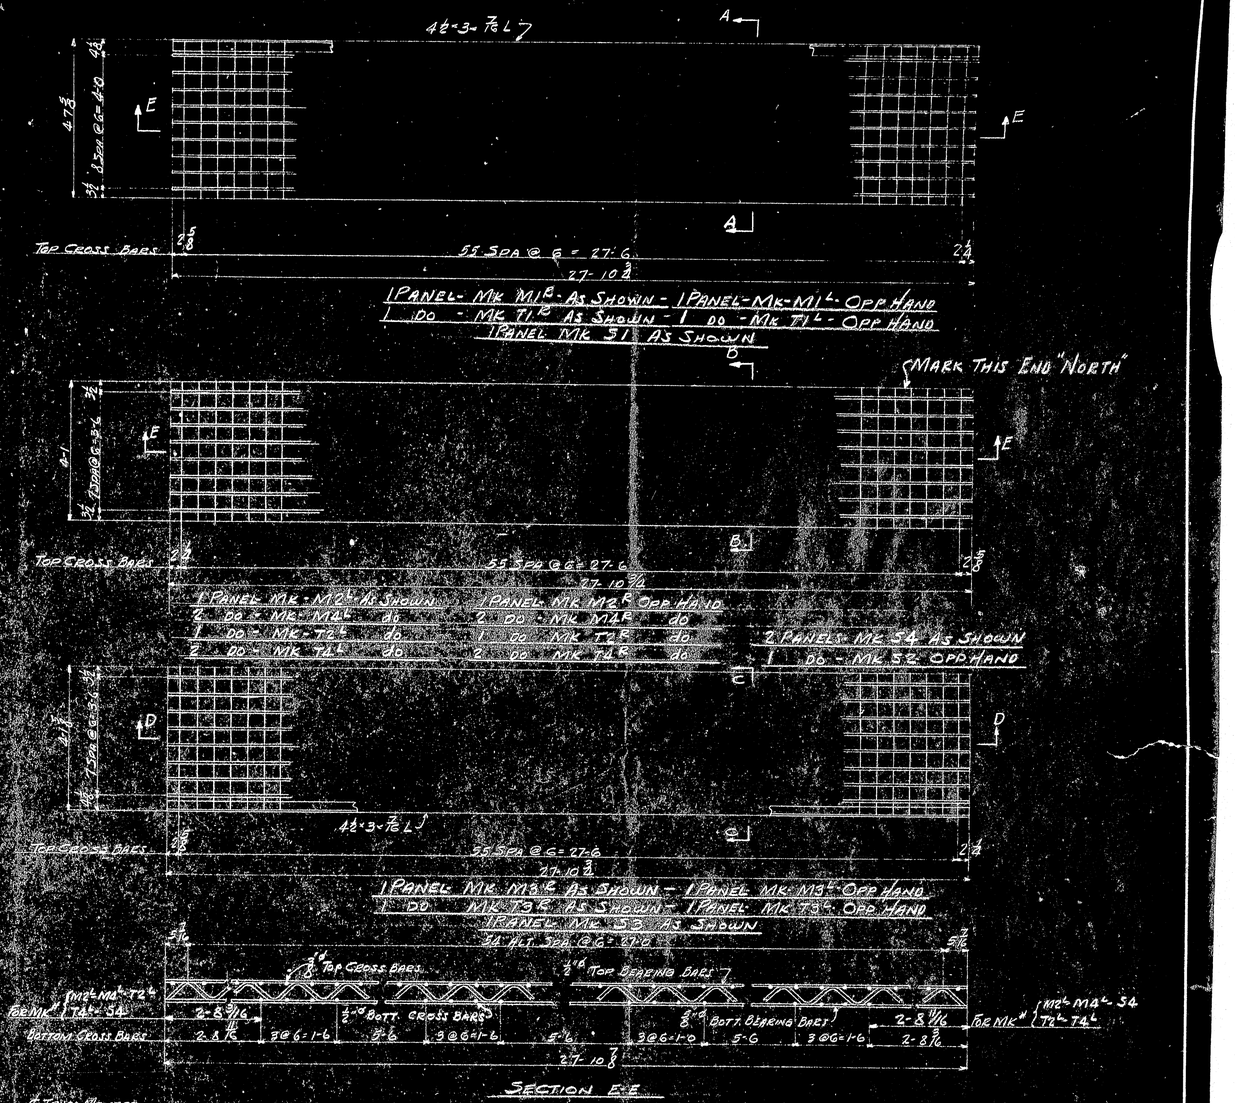

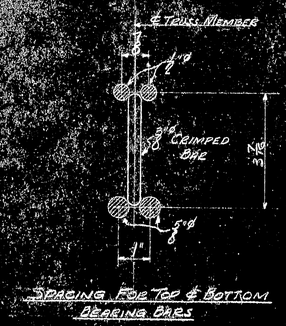

Note. For Form Ie Spacing See Dwg 3031-8 For other notes see Dwg 3031-1

Bill of Material

Panel Mark	No Top Bearing Bars	Length	No Bott Bearing Bars	Length	No Bott Cross Bars	Length	No Bars Diagonal Bars	Length	1/2" Bars Length	3/8" Angles 4 x 3 x 7/16 Length
K1E-P1E-R1	90	27-11 3/8	90	27-11 3/8	280	4-7/8	80	4-6 3/4	45	31-10	5	27-11 3/8
K2-P2E-R2	240	27-11 3/8	240	27-11 3/8	960	4-1	240	4-1	120	31-10	15	27-11 3/8
K3E-P3E-R3	80	27-11 3/8	80	27-11 3/8	280	4-1/8	80	4-0 3/4	40	31-10	5	27-11 3/8
M1E-T1E-S1	90	27-10 3/8	90	27-10 3/8	280	4-7/8	80	4-6 3/4	45	31-10	5	27-10 3/8
M2-S2-T2-T4	240	27-10 3/8	240	27-10 3/8	960	4-1	240	4-1	120	31-10	15	27-10 3/8
M3E-T3E-S3	80	27-10 3/8	80	27-10 3/8	280	4-1/8	80	4-0 3/4	40	31-10	5	27-10 3/8

		Customer	The Phoenix Bridge Co. Phoenixville, Penna.
G.W.H	7-20-38	Customer Order No.	
L.M.	6-23-38	Reference	
Revised	Date		

PBF Appl. Dwg

Reliance Steel Products Company

Rankin, (Pittsburgh District) Pa. Bridge Department

Project	P.W.A. Project ME 1010 D		
Location	Deer Isle-Sedgwick Bridge, Hancock County, Me.		
Drawn	L.M. 5-23-38	Approved By	
Checked	G.W.H. 5-27-38	Dwg. No.	3031-6
Traced		Contract No.	G 3328
