



Semi-Annual Progress Report

BOEM Lease OCS-A 0553

August 31, 2025

Submitted to:
Bureau of Ocean Energy
Management
1849 C Street NW
Washington, D.C. 20240

Submitted by:
Maine Governor's Energy Office

TABLE OF CONTENTS

LIST OF TABLES	1
1.0 INTRODUCTION	1
1.1 PROJECT OVERVIEW	1
2.0 PROJECT PROGRESS	2
2.1 SITE CHARACTERIZATION AND TRANSMISSION PLANNING ACTIVITIES.....	2
2.2 OTHER DEVELOPMENT ACTIVITIES.....	7
3.0 ENGAGEMENT	7
4.0 STATE OF SCIENCE	11
APPENDIX A FEDERAL & STATE AGENCIES MEETING LOG	A-1

LIST OF FIGURES

Figure 1: Gulf of Maine Research Lease Area	2
Figure 2: Desktop evaluation of potential export cable routes. Green=most feasible, Red=least	4
Figure 3: Aerial digital survey transects in the Gulf of Maine and RFCI	5

LIST OF TABLES

Table 1: Progress on the Research Framework by Category	11
Table A-1: Log of Federal and State Agencies Meetings, July 2022 through February 2025	A-1

MAINE RESEARCH ARRAY

SEMI-ANNUAL PROGRESS REPORT

Research Lease OCS-A 0553

August 31, 2025

ABBREVIATIONS

ACP	Agency Communication Plan
BOEM	Bureau of Ocean Energy Management
DGC	Diamond Generating Corporation
DMR	Maine Department of Marine Resources
DOW	Diamond Offshore Wind
FCP	Fisheries Communication Plan
FLiDAR	Floating (buoy-based) light imaging, detection, and ranging
Ft	feet
GEO	Maine Governor's Energy Office
MeRA	Maine Research Array
MOSWRC	Maine Offshore Wind Research Consortium
NATCP	Native American Tribes Communication Plan
NEPA	National Environmental Policy Act
NERACOOS	Northeast Regional Association of Coastal Ocean Observing Systems
NMFS	National Marine Fisheries Service
NOAA	National Oceanic and Atmospheric Administration
NREL	National Renewable Energy Laboratory
OCS	Outer Continental Shelf
PTOW	Pine Tree Offshore Wind
RAP	Research Activities Plan
USFWS	U.S. Fish and Wildlife Service
UMaine	University of Maine
U.S.	United States
WTG	wind turbine generator

MAINE RESEARCH ARRAY

SEMI-ANNUAL PROGRESS REPORT

Research Lease OCS-A 0553

August 31, 2025

1.0 INTRODUCTION

This Progress Report is prepared in accordance with Research Lease OCS-A 0553 (Lease Area), which requires a Progress Report to the Bureau of Ocean Energy Management (BOEM) every six months through the Research Activities Plan (RAP) preparation and approval process. This Progress Report covers the reporting period March 1, 2025, through August 31, 2025. As required by Addendum C, Section 4.1 of the Lease, this Progress Report summarizes overall project progress and engagement activities undertaken with agencies, Native American Tribes, communities, ocean user groups, and the general public over the reporting period, and plans for continued engagement.

1.1 PROJECT OVERVIEW

The State of Maine (State) was awarded a Research Lease for the Lease Area in the Gulf of Maine by BOEM for the purpose of developing and operating the Maine Research Array project (MeRA or Project). The Lease Area is located approximately 35 miles from shore, in water depths of approximately 150-200 m (Figure 1). Pine Tree Offshore Wind (PTOW) is the Designated Operator for the MeRA.

The objective of the Project is to create a set of informed best practices and standards for commercial-scale floating offshore wind projects in the Gulf of Maine, nationally and internationally, to utilize in planning, permitting, constructing and operating commercial-scale projects in a fashion that optimizes co-existence with traditional marine users and the ecosystem. Research conducted at the Project will also support the advancement of Maine's floating offshore wind supply chain and workforce. More information about the State's Offshore Wind initiative can be found on the website of the Governor's Energy Office (GEO): <https://www.maine.gov/energy/initiatives/offshorewind>.

The Project is intended to be a small-scale array of wind turbines that is large enough to evaluate many of the issues associated with commercial-scale floating wind turbine arrays built and operated in the Gulf of Maine. The Project is anticipated to consist of 12 or fewer wind turbines, producing no more than 144 megawatts of electricity.

The total acreage of the initial Lease Area is approximately 14,945 acres, which allows room for considering layout alternatives and micro-siting of the floating turbines and anchor systems to avoid and buffer any sensitive resources that may be discovered during surveys. The Lease allows an area of no more than 9,700 acres to be proposed for development in the Project's Research Activities Plan (RAP). Following approval by BOEM of the RAP, the State will relinquish those portions of the Lease Area that are not included in the proposed development.

As proposed, the Project will use floating offshore wind platform technology designed by the University of Maine (UMaine). The Advanced Structures and Composites Center at UMaine has been a pioneer in the development of floating offshore wind platforms and holds over 70 floating turbine patents.

MAINE RESEARCH ARRAY

SEMI-ANNUAL PROGRESS REPORT

Research Lease OCS-A 0553

August 31, 2025

Ongoing information about the Project including notices to mariners and updates of survey and pre-construction activities can be found on the MeRA website, <https://www.maineresearcharray.com>.

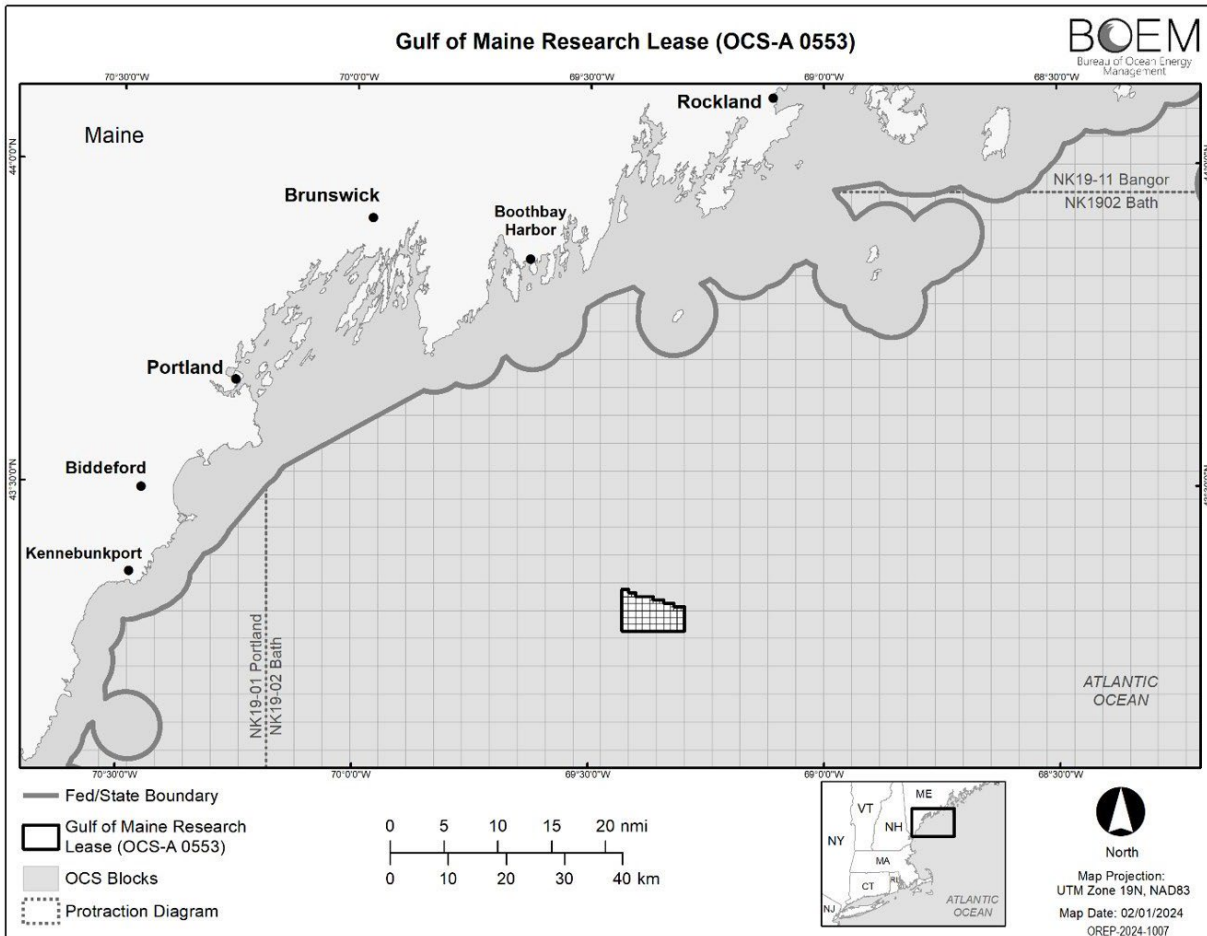


Figure 1: Gulf of Maine Research Lease Area

2.0 PROJECT PROGRESS

This section provides a summary of MeRA Project-related site characterization and development activities conducted from prior to lease issuance through the current progress reporting period.

2.1 SITE CHARACTERIZATION AND TRANSMISSION PLANNING ACTIVITIES

MeRA partners have been working on plans for site assessment and characterization activities, such as wind resource and metocean monitoring, geophysical and geotechnical (G&G) surveys, benthic surveys, surveys of marine biota, and terrestrial surveys since 2021. The following is a summary of the work completed to date and anticipated next steps.

MAINE RESEARCH ARRAY

SEMI-ANNUAL PROGRESS REPORT

Research Lease OCS-A 0553

August 31, 2025

Wind Resource / Metocean Monitoring

In 2021 PTOW developed an initial, desktop energy production estimate (EPE) for the Project using UMaine's existing DeepC LiDAR buoy data, along with information from the turbine OEM. PTOW also commissioned a desktop metocean study for the site including wind conditions, wave conditions, current conditions and other metocean parameters such as water temperature, salinity, visibility, and air and sea density.

Early in 2022 PTOW began planning and preparations for deployment of a metocean and Floating Light Detection and Ranging (FLiDAR) buoy to gather site-specific wind, weather and oceanographic data. In planning the buoy, PTOW and its environmental consultants sought input from federal and state resource Agencies regarding methods and types of biological instrumentation to be deployed on the buoy, including technology for monitoring marine mammals, fish, birds and bats (Appendix A).

PTOW applied for and in October 2024 obtained U.S. Army Corps of Engineers approval for deployment of a FLiDAR buoy at one of five locations within or adjacent to the Lease Area. Deployment of the buoy is expected to occur following the execution of a Power Purchase Agreement (PPA) with the Maine Public Utilities Commission (PUC). PTOW will coordinate with the U.S. Coast Guard and other applicable Agencies to obtain other necessary permits, authorizations and approvals before deploying the buoy.

MAINE RESEARCH ARRAY

SEMI-ANNUAL PROGRESS REPORT

Research Lease OCS-A 0553

August 31, 2025

Geophysical and Benthic Surveys

In 2022 PTOW commissioned a desktop geologic study covering the Lease Area and prospective cable route / landfall configurations. As expected, the areas evaluated include areas of soft soils, hard ground, bedrock, and both gradual and steep slopes. Multiple potential cable routes to two prospective interconnection locations were identified. These were evaluated and color-coded based on their relative feasibility (Figure 2).

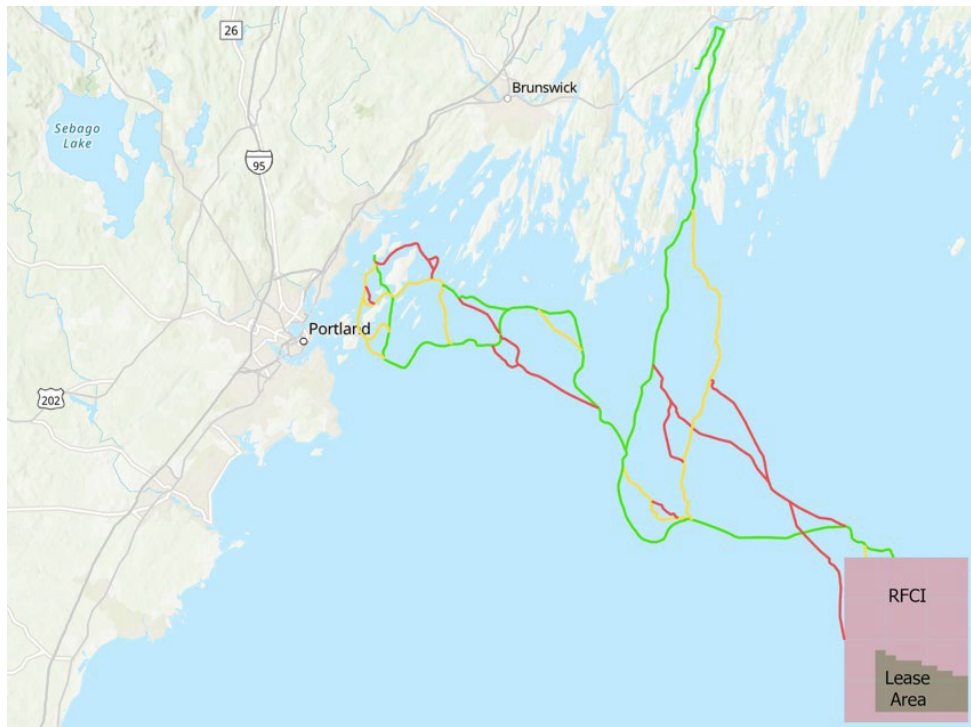


Figure 2: Desktop evaluation of potential export cable routes. Green=most feasible, Red=least.

Additional data will be gathered during site investigation surveys to select and optimize preferred anchor arrangements and cable route options that avoid and minimize the potential for adverse impacts to benthic habitats.

The next step in this process will be a Reconnaissance Geophysical and Benthic Survey for which planning is in progress. The survey will include the Lease Area and the area surrounding the most feasible and least impactful cable route options as indicated by the desktop analysis. Planning has included solicitation and selection of the geophysical and benthic survey teams, and consultations with BOEM and other federal and state resource agencies (Appendix A). PTOW has prepared draft survey plans that will be finalized for BOEM review once the survey schedule has been determined. High-resolution geophysical and geotechnical surveys will be conducted following selection of a preferred project layout, cable route and anchor locations.

MAINE RESEARCH ARRAY

SEMI-ANNUAL PROGRESS REPORT

Research Lease OCS-A 0553

August 31, 2025

Digital Aerial Surveys

From May 2023 through February 2024 PTOW sponsored four quarterly digital aerial wildlife surveys of the Request for Competitive Interest (RFCI) area, plus a buffer (Figure 3).



Figure 3: Aerial digital survey transects in the Gulf of Maine and RFCI

These surveys were conducted in conjunction with BOEM-sponsored surveys of a much larger area of the Gulf of Maine. PTOW's transects were closer together than the Gulf-wide transects and designed to be in accordance with BOEM guidance.

The surveys were conducted by the Biodiversity Research Institute (BRI) and HiDef Aerial Surveying (HiDef), using HiDef's GEN 2.5 survey rig mounted in a fixed-wing aircraft, which is designed specifically for high quality seabird and marine mammal surveys. The rig contains four extremely high-resolution digital video cameras, and surveys are flown at ~400 m altitude at a ground speed of 220 kph (~120 knots), providing imagery at 1.5 cm ground sample distance (GSD). These surveys collected data on the distribution and abundance of a range of taxonomic groups, including seabirds, marine mammals, and fish, as well as fishing activities. The images from the surveys are in the process of being analyzed and the observations tabulated by BRI. A final report is expected in the coming months.

DMR Research Surveys

Maine DMR submitted a research survey plan to BOEM on March 31, 2025, after having two pre-Survey Plan meetings with BOEM on February 3 and March 17, 2025. Maine DMR met with BOEM and GEO several more times throughout the process including on May 13 and June 11, 2025 to check on the status of the Survey Plan review by BOEM. DMR received the first round of feedback and

MAINE RESEARCH ARRAY

SEMI-ANNUAL PROGRESS REPORT

Research Lease OCS-A 0553

August 31, 2025

comment matrix from BOEM on the Survey Plan on June 12, 2025. DMR submitted their revisions and responses back to BOEM on June 23, 2025. The second round of feedback and comment matrix was sent to DMR on July 10, 2025 who submitted their revisions and responses back to BOEM on July 11, 2025. DMR received BOEM email acceptance of the research Survey Plan on July 15, 2025. DMR sent notifications to fishing stakeholders, mariners, and Tribes pursuant to lease requirements. This included sending out notices of the Summer bottom trawl survey on April 9 and June 9, 2025 and all other summer surveys on April 12, 2025. DMR also held an information meeting for Tribes on Zoom on April 30, 2025. On July 23, 2025, DMR began the research trawl surveys within and around the research lease as described in the approved survey plan. DMR sent out the first notice for the fall bottom trawl survey on July 29, 2025 and the first notice for all other fall surveys on August 5, 2025. The surveys are following the Maine Offshore Wind Fisheries Working group recommendations to maximize baseline monitoring. Research survey work is anticipated through summer 2027 but will depend on Survey Plan submittal and acceptance each year.

DMR's planned surveys include oceanographic monitoring; zooplankton and larval lobster survey; seafloor mapping and characterization; bottom trawl survey; active acoustic survey; highly migratory species monitoring; passive acoustic monitoring; ecosystem modeling; and socio-economic and local historical knowledge survey.

In addition to collecting important baseline data in a previously data-poor area, it allows the survey teams to test gear, conduct trial runs, and ensure protocols and processes are clear so when construction is approaching, the state is ready to continue conducting surveys.

2.2 OTHER DEVELOPMENT ACTIVITIES

Preliminary Engineering

The PTOW team has performed a pre-Front-End Engineering (pre-FEED) study for MeRA, including preliminary WTG, floating foundation and mooring sizing, preliminary cable sizing and conceptual routes, and preliminary points of interconnect with conceptual layouts for onshore facilities. The initial engineering effort explored founding the WTG on the University of Maine's (UMaine) VoltturnUS semi-submersible concrete floating foundation secured to the seabed via mooring lines and embedded anchors. The patented VoltturnUS technology has undergone over a decade of research and development, including deploying a scaled prototype that underwent 18 months of operation and testing at a site off the coast of Castine, ME, making it a sound choice for the Project. The University of Maine is currently testing the next generation of the VoltturnUS technology, called the VoltturnUS+, which is also deployed off the coast of Castine through 2026.

3.0 ENGAGEMENT

MeRA has been conducting strategic stakeholder and community outreach for the last few years as we laid the groundwork for, and sited, the project with extensive input from fishing communities, Tribes, and other stakeholders. On a broader level, we've been engaging with stakeholders on the coast and statewide since 2020 to establish foundational support for Maine's responsible offshore wind industry. During the early phases of permitting and regulatory processes, our approach has been steady and targeted. We have focused on building relationships with eNGOs, industry groups, and maritime interests, and making information and resources available to the public and our partners.

In August of 2022, MeRA launched the [MeRA Project](#) website that has served as a centralized information hub. This platform has received a high level of engagement, with thousands of visits and page views. The most frequently viewed pages are the Project page and the Collaboration page, which offer extensive detail on the robust stakeholder participation involved in developing MeRA, and the economic and environmental benefits MeRA will bring to the state of Maine. This website also has a news portal providing information on planning and progress.

Due to the uncertainties in the U.S. offshore wind industry, the MeRA project has maintained but not expanded engagement. MeRA partners continue to provide timely updates to the fishing industry, Tribes, agencies, and stakeholders during relevant public meetings, such as the Advisory Board meetings of the Maine Offshore Wind Research Consortium, and through notifications and newsletters. Additional engagement will continue commensurate to the MeRA advancement. Baseline surveys may continue but additional work is not expected to be significant for some time.

MAINE RESEARCH ARRAY

SEMI-ANNUAL PROGRESS REPORT

Research Lease OCS-A 0553

August 31, 2025

Federal and State Agencies

MeRA partners submitted an initial draft MeRA Agency Communication Plan (ACP) to BOEM on December 20, 2024. The [ACP](#) has been made available for public review and comment on the MeRA Project website. During the current reporting period PTOW confirmed agency points of contact with permitting and environmental review authority. These lists will be updated as the Project progresses, and as further feedback is received from the Agencies.

MeRA partners maintain frequent and regular contact regarding Agency engagement and communications activities. GEO and PTOW have hosted and participated in project-related meetings with Agencies since at least July 2022 (Appendix A).

During this early stage of project development, the Project outreach goals have been to establish points of contact, open lines of communication, introduce the MeRA Project, and discuss future surveys and site characterization approaches. Although developer surveys are not anticipated in the near future, any draft surveys plans will be submitted for Agency and BOEM review before survey activities commence pursuant to lease requirements.

In parallel with MeRA planning, the Maine Department of Marine Resources (DMR) has begun conducting baseline and monitoring surveys within and around the Project area. The State's surveys are focused on meeting the goals of the Maine Offshore Wind Research Framework and the recommendations by the Fisheries and Environment & Wildlife Working Groups for the Maine Offshore Wind Roadmap. DMR held pre-survey meetings on the survey plan with BOEM on multiple dates listed in Appendix A.

Additionally, GEO, DMR, PTOW and BSEE met on March 27, 2025 to review safety requirements during survey operations. PTOW submitted the "Performance Measures Data – Renewable Energy" Form 1014-0034 with safety performance for calendar year 2024 to BSEE on March 27, 2025 pursuant to federal requirements.

The State has been drafting a Data Dissemination Plan in consultation and coordination with BOEM. The Plan will be a living document that meets all requirements and evolves as the Project progresses.

MeRA anticipates the next reporting period will also include:

- Providing Agencies, including local government agencies, with opportunities to review and comment on proposed survey plans and other aspects of Project development, as appropriate;
- Identifying local government agencies and their contact information as applicable to the very early stages of the project;
- Informing and coordinating with stakeholders on future survey activities; and
- Considering opportunities for collaboration during future site characterization surveys.

Native American Tribes

PTOW submitted an initial draft MeRA Native American Tribes Communication Plan (NATCP) to

MAINE RESEARCH ARRAY

SEMI-ANNUAL PROGRESS REPORT

Research Lease OCS-A 0553

August 31, 2025

BOEM on December 20, 2024. The initial draft NATCP has been made available for public review and comment on the [MeRA Project website](#), and notification of its availability has been sent to Tribal points of contact.

While drafting the NATCP, PTOW reached out on November 19, 2024 to the eleven Tribes identified by BOEM that may have an interest in participating in the engagement process for the Project, and that may have ancestral ties to the Project area, which encompasses the PTOW wind lease site and possible cable corridors and interconnections to shore, as well as the broader Gulf of Maine area. Please see page 10 of the [NATCP](#) for the list of eleven tribes. Five of the eleven Tribes are located in Maine, and the remaining six are located in New York, Rhode Island, Connecticut and Massachusetts. Of the eleven Tribes, three responded to the correspondence from PTOW. The Mi'kmaq Nation provided a new point of contact. The two Passamaquoddy Tribes – the Pleasant Point Reservation and the Indian Township Reservation – responded through their attorneys expressing strong interest in engaging regarding the Project.

Given the Passamaquoddy Tribes' response, PTOW scheduled an introductory call on December 9, 2024, which was attended by Chiefs from both Reservations, the Passamaquoddy's attorneys and other Tribal representatives. During this call the Tribes' attorneys were designated as the points of contact for the Passamaquoddy. Communication with the attorneys continued after the call and an in-person meeting with the Passamaquoddy Tribes will be scheduled upon request.

On January 29, 2025, PTOW emailed all the Tribes again informing them that the initial draft NATCP had been provided to BOEM in December and was now posted and available for review and comment on the MeRA website, with a link provided. On March 31, 2025, DMR sent an email invitation to all Gulf of Maine Tribes in the NATCP for a pre-survey meeting. Certified letters with details of the meeting were mailed to each Tribe on April 11, 2025, and a final email reminder about the meeting was sent on April 29, 2025. DMR held the meeting using Microsoft Teams on April 30, 2025. Two representatives of the Houlton Band of Maliseet Indians Tribe attended the Zoom meeting. On August 8, 2025, GEO sent an email to all Tribes listed in the NATCP informing them that Stephanie Watson, GEO Offshore Wind Program Manager, will be their Point of Contact on the Project and provided contact information.

Fisheries

PTOW submitted an initial draft MeRA [Fisheries Communication Plan \(FCP\)](#) to BOEM on December 20, 2024. The initial draft of the FCP has been made available for public review on the [MeRA Project website](#). The FCP includes an initial list of fishing sectors and organizations that are potentially affected by the project starting on page 7. Because the Project is at an early planning stage, a Fisheries Liaison, Fisheries Representative and Onboard Fisheries Liaisons have not yet been named. These roles will be filled as the Project makes further commercial progress, and well in advance of any planned or anticipated survey or outreach activities.

In the interim, PTOW has engaged a fisheries consultant on the Project since August of 2020 who has participated in stakeholder liaison and engagement activities. This engagement has included

MAINE RESEARCH ARRAY

SEMI-ANNUAL PROGRESS REPORT

Research Lease OCS-A 0553

August 31, 2025

participation in fisheries stakeholder meetings held by BOEM, Maine DMR, and the Maine GEO and includes the efforts of the Maine Offshore Wind Roadmap, Offshore Wind Port Advisory Group, and the Maine Offshore Wind Research Consortium. PTOW's fisheries consultant has also joined in meetings and communications with fisheries participants and their advocates to better understand fishing activity, solicit input, refine site location, and address questions outside of public meetings and webinars.

DMR provided pre-survey notifications to fishermen and other interested parties in compliance with the lease. Each quarter, DMR has provided a notice with details of what surveys are expected to occur, including anticipated frequency and survey equipment that will be used. In addition, prior to beginning the bottom trawl survey, notice is provided that includes a tentative time lime, vessel details, number of tows anticipated, and a point of contact for more information

MAINE RESEARCH ARRAY

SEMI-ANNUAL PROGRESS REPORT

Research Lease OCS-A 0553

February 28, 2025

4.0 STATE OF THE SCIENCE

The State of Maine and other researchers are in the beginning stages of utilizing the research array to conduct and disseminate critical research to inform the future production, transportation, or transmission of renewable energy from floating offshore wind turbines. The research activities will advance priorities from the Research Framework in the lease application, as identified by key experts and stakeholders in the Gulf of Maine (Table 1).

Table 1: Progress to Date on the Research Framework by Category (Stipulation 4.1.1)

Research Category	Planned Research (Anticipated Funding Mechanism)	Current Research (Funding Mechanism)	Completed Research (Funding Mechanism)	Data Dissemination
Fisheries				
			Exploring Approaches to Fisheries Coexistence with Floating Offshore Wind in the Gulf of Maine (Maine Offshore Wind Research Consortium or “Consortium”) – Desktop study with three stages of fisheries engagement (Completed 2024)	Consortium Website GMRI Website Presentation at the 2024 Maine Fishermen’s Forum Presentation at Research Consortium webinar in April 2024 Presented on a panel and a poster at 2024 AFloat Conference in September 2024 Presented poster at 2024 ACP Offshore Wind Conference in October 2024 Presented interim findings to Advisory Board in November 2024 Final presentation to the Advisory Board in February 2025
Ecosystem and Environment				

MAINE RESEARCH ARRAY

SEMI-ANNUAL PROGRESS REPORT

Research Lease OCS-A 0553

February 28, 2025

	Offshore Bat Monitoring (Maine Offshore Wind Research Consortium) – field data collection and data analysis (anticipated 9/25 – 12/26)			
	Secondary Entanglement Risk and Technology Assessment (Maine Offshore Wind Research Consortium) – Literature review, data gap analysis, desktop risk assessment, stakeholder engagement, and technology recommendations (anticipated 9/25 – 3/26)			
Socioeconomic Impacts				
			Socioeconomic Data Inventory (Maine Offshore Wind Research Consortium) (desktop research, data gap analysis, and stakeholder engagement) (Completed 2024)	Consortium Website and Report Presentation at the 2024 Maine Fishermen’s Forum Presentation at Research Consortium webinar in April 2024 Presented on a panel at the 2024 Afloat Conference in September 2024 Final presentation to the Advisory Board in July 2024
	Assessment of social, economic,			

MAINE RESEARCH ARRAY

SEMI-ANNUAL PROGRESS REPORT

Research Lease OCS-A 0553

February 28, 2025

	and cultural impacts of floating offshore wind development on Maine’s fishing industry (Maine Offshore Wind Research Consortium) - Assessment of direct economic impacts and sociocultural impacts – with stakeholder engagement (anticipated 9/25 – 3/26)			
Workforce Development				
Navigation				
Technology Development				
	Secondary Entanglement Risk and Technology Assessment (Maine Offshore Wind Research Consortium) – Literature review, data gap analysis, desktop risk assessment, stakeholder engagement, and technology recommendations (anticipated 9/25 – 3/26)	VoltumUS+ research, technology, workforce and supply chain development at ¼ scale demonstration. Deployment May 2025 – December 2026 in state waters off Castine, Maine (state funding – non-Consortium)		

SEMI-ANNUAL PROGRESS REPORT

Research Lease OCS-A 0553

February 28, 2025

Appendix A FEDERAL & STATE AGENCIES MEETING LOG

Table A-1: Log of Federal and State Agencies Meetings, July 2022 through August 2025

Date	Agencies in Attendance	Topic
July 29, 2022	Maine DMR	Team intros and pre-permitting data coordination
September 8, 2022	Maine DMR, Maine GEO	G+G survey and stakeholder outreach planning
October 21, 2022	Maine DMR, Maine IFW	Team intros and baseline survey planning
January 25, 2023	Maine DMR, Maine GEO	Project location and layout workshop
February 13, 2023	BOEM, Maine GEO, Maine DMR	Research Lease kick-off
February 15, 2023	Maine DMR	Baseline surveys coordination
February 24, 2023	USFWS, Maine Seabird Islands NWR	Gulf of Maine seabird tracking
March 9, 2023	BOEM, NOAA, Maine GEO, Maine DMR	RFCI siting
March 15, 2023	Maine DMR Trawl Team	Trawl survey coordination
March 20, 2023	NOAA – NFSC, GARFO	Team and project intros, baseline survey planning, opportunities for input and collaboration
March 21, 2023	USFWS Maine Field Office and Maine Coastal Islands NWR	Project intro, timeline, and planned avian and bat surveys
April 3, 2023	Maine Offshore Wind Research Consortium (OSWRC), Advisory Board	Research priorities and funding
April 7, 2023	Maine DMR	FLiDAR buoy acoustics planning
April 25, 2023	USFWS - Maine Field Office, Maine Coastal Islands NWR, and Migratory Birds, Maine IFW	Motus and other tagging options for baseline surveys
April 27, 2023	BOEM, Maine GEO	Initiate biweekly update calls
May 10-11, 2023	BOEM, NOAA	Gulf of Maine Task Force
May 15, 2023	U.S. Navy	Navy ship trials mitigation planning (NEAV)
June 8, 2023	BOEM, GEO	Biweekly update call
June 15, 2023	Maine OSWRC, Advisory Board	Research priorities and funding
June 27, 2023	BOEM, NOAA, USCG, Maine GEO, Maine DMR	Spatial analysis re: shipping lanes and fairways
July 12, 2023	Maine GEO, Maine DMR	Lease area configurations
July 17, 2023	Maine OSWC micrositing subgroup	Array micrositing planning
July 24, 2023	Maine GEO, Maine DMR	Lease area configurations
August 3, 2023	BOEM, GEO	Biweekly update call
August 8, 2023	BOEM, Maine OSWC, Maine GEO, Maine DMR, UMaine, NERACOOS, NYSERDA	Baseline survey scoping
August 10, 2023	USFWS Maine Coastal Islands NWR, Maine OSWRC, Maine IFW, Maine DMR	Avian and bat baseline survey scoping
August 29, 2023	BOEM, GEO	Biweekly update call
September 6, 2023	Maine OSWRC, Advisory Board	Research priorities and funding
September 8, 2023	Maine GEO, Maine DMR	Biological survey scoping and federal Agency engagement
September 12, 2023	NOAA Fisheries	IHA Pre-application meeting for Recon G+G/Benthic surveys
September 14, 2023	BOEM, GEO	Biweekly update call
September 28, 2023	BOEM, GEO	Biweekly update call

MAINE RESEARCH ARRAY

SEMI-ANNUAL PROGRESS REPORT

Research Lease OCS-A 0553

February 28, 2025

Date	Agencies in Attendance	Topic
October 13, 2023	Maine GEO	Data dissemination plan
October 13, 2023	Maine GEO, Maine DMR	Fisheries Communication Plan
November 1, 2023	Maine GEO	Data dissemination plan
November 13, 2023	BOEM, NOAA, Maine DMR	Survey info for BOEM EA
November 13, 2023	NOAA, Maine DMR	G+G surveys update
November 17, 2023	Maine DMR, Maine IFW, UMaine, NOAA	DMR data sharing and collaboration workshop
November 20, 2023	BOEM, BSEE	Digital aerial surveys update
November 28, 2023	Maine OSWRC, Advisory Board	Research priorities and funding
December 1, 2023	Maine DMR, UMaine	Available data to inform G+G and benthic surveys
January 19, 2024	Army Corps of Engineers	FLiDAR permitting
February 1, 2024	Army Corps of Engineers	FLiDAR permitting
February 27, 2024	Maine OSWRC, Advisory Board	Research priorities and funding
<i>Ongoing March 2024 – Present</i>	Maine GEO, Maine DMR	Weekly Project update calls
March 7, 2024	Maine OSWRC	Co-use conflict reduction
March 8, 2024	Maine OSWRC	Technology development
March 12, 2024	Maine OSWRC	Impact on ecosystems
March 13, 2024	Maine OSWRC	Socio-economic
April 3, 2024	Maine OSWRC	FOSW technology
April 4, 2024	Maine GEO, Maine DMR	Project updates
April 5, 2024	Maine OSWRC	Wildlife & groundfish
April 12, 2024	Army Corps of Engineers	FLiDAR permitting
May 3, 2024	Army Corps of Engineers	FLiDAR permit conditions
May 6, 2024	Maine OSWRC, Advisory Board	Research priorities and funding
May 10, 2024	Maine GEO, Maine DMR	Data sharing plan
May 20, 2024	Maine GEO, Maine DMR	Data sharing plan
May 23, 2024	Maine GEO, Maine DMR	Data sharing plan
June 21, 2024	Maine OSWRC, Advisory Board	Research priorities and funding
July 3, 2024	NREL, BOEM, NOAA, Maine GEO, NYSERDA	Advisory Board - NREL's Solutions for U.S. Floating Offshore Wind Farms and Fishing Compatibility
July 3, 2024	Maine GEO, Maine DMR	Data sharing plan
July 22, 2024	Maine OSWRC, Advisory Board	Research priorities and funding
September 5, 2024	Maine DMR, Maine IFW, UMaine, NOAA	DMR data sharing and collaboration workshop
September 6, 2024	Army Corps of Engineers	FLiDAR permitting
October 4, 2024	NREL, BOEM, NOAA, Maine GEO, NYSERDA	Advisory Board – NREL's Solutions for U.S. Floating Offshore Wind and Fishing Compatibility
October 25, 2024	BOEM, Maine GEO	Maine Research Lease Kick-Off Call
November 22, 2024	Maine OSWRC, Advisory Board	Research priorities and funding
December 12, 2024	BOEM, Maine GEO	Maine Research Lease check-in
December 18, 2024	BOEM, Maine GEO	Draft communications plans update
January 17, 2025	Maine OSWRC, GEO, DMR	Research and surveys update
January 28, 2025	NREL, BOEM, NOAA, Maine GEO, NYSERDA	Project Advisory Board Meeting - Co-Design Solutions for U.S. Floating Offshore Wind and Fishing Compatibility
February 3, 2025	Maine OSWRC	Socio-economic impacts and community benefit discussion
February 3, 2025	BOEM, Maine GEO and DMR	ME Research Lease Survey Plan Discussion
March 17, 2025	BOEM, Maine GEO and DMR	ME Research Lease Survey Plan Discussion
March 27, 2025	Maine GEO, DMR, PTOW, BSEE	Safety During Survey Operations Discussion

MAINE RESEARCH ARRAY

SEMI-ANNUAL PROGRESS REPORT

Research Lease OCS-A 0553

February 28, 2025

April 30, 2025	Maine GEO, DMR, Tribes as listed in NATCP	ME Research Lease Pre-Survey Planning Meeting
June 11, 2025	BOEM, Maine GEO and DMR	ME Research Lease Survey Plan Discussion – PSOs and trained lookouts
August 7, 2025	BOEM, Maine GEO	Check In and Data Dissemination Plan Discussion
<i>Ongoing Feb 6, 2025 - Present</i>	BOEM, Maine GEO	Biweekly or As Needed Project update calls
