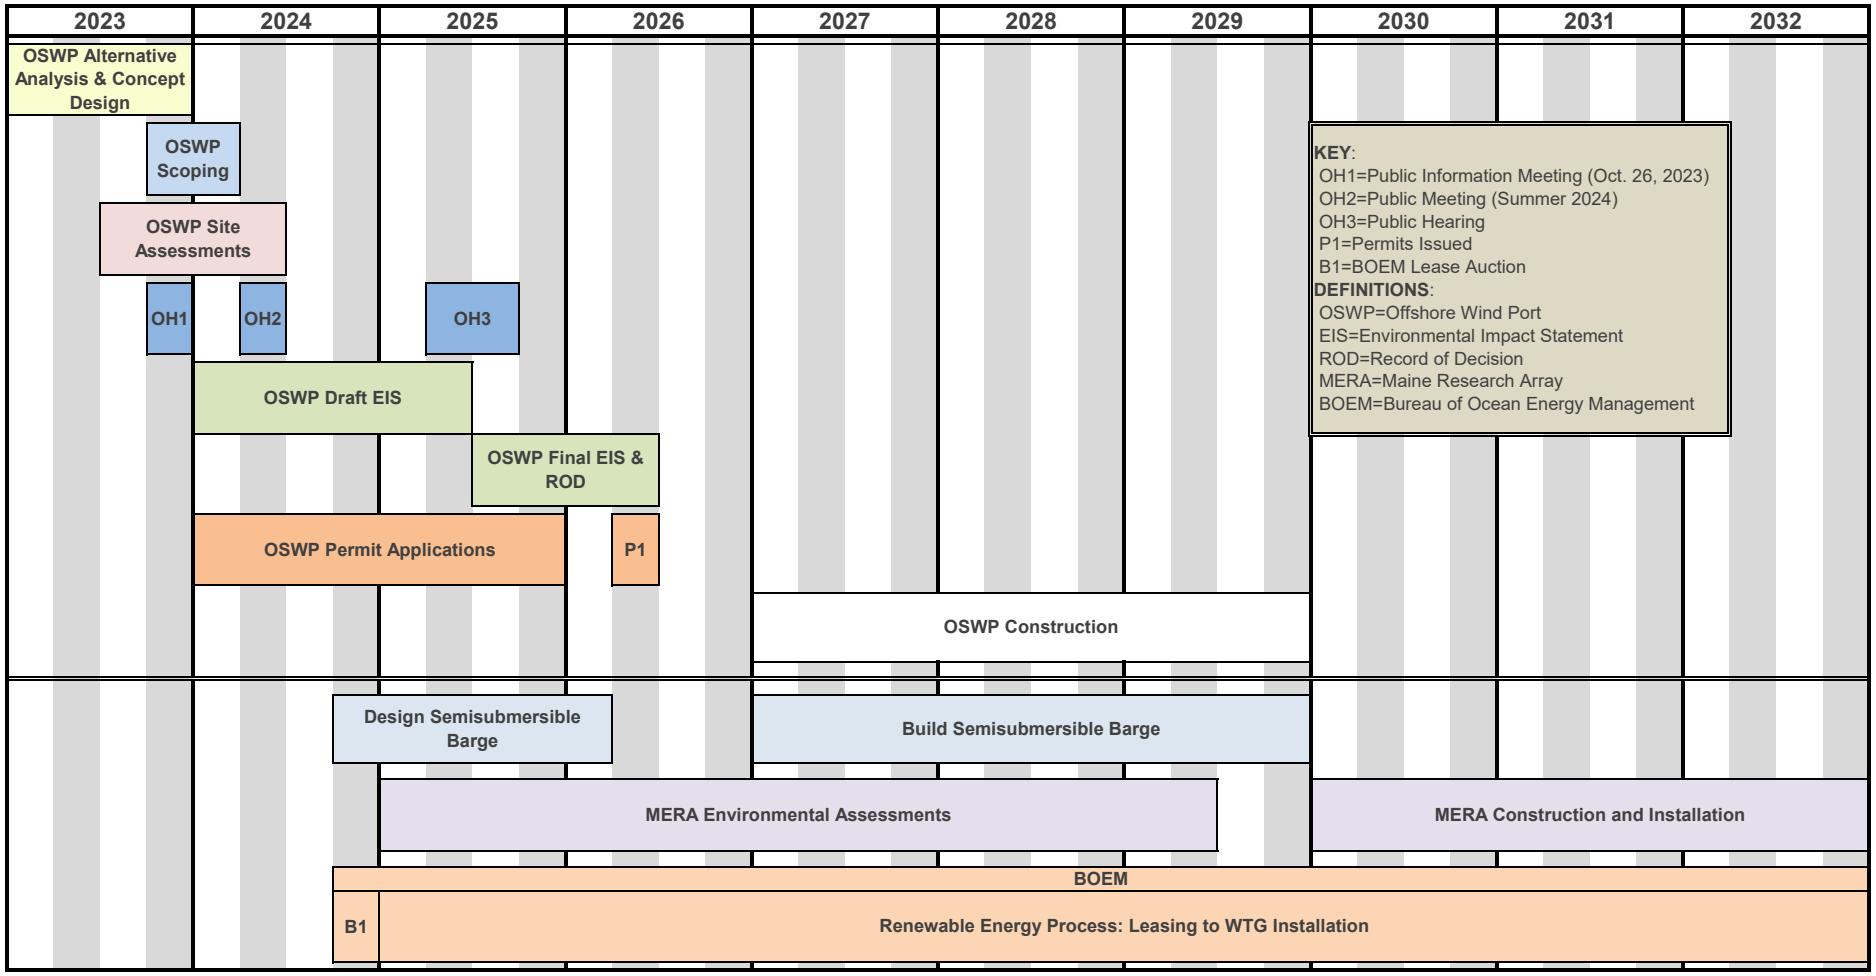
2023
2024
2025
2026
2027
2028
2029
2030
2031
2032
OSWP Alternative Analysis & Concept Design
OSWP Scoping
OSWP Site Assessments
OH1
OH2
OH3
OSWP Draft EIS
OSWP Final EIS & ROD
OSWP Permit Applications
P1
OSWP Construction
KEY:
OH1=Public Information Meeting (Oct. 26, 2023)
OH2=Public Meeting (Summer 2024)
OH3=Public Hearing
P1=Permits Issued
B1=BOEM Lease Auction
DEFINITIONS:
OSWP=Offshore Wind Port
EIS=Environmental Impact Statement
ROD=Record of Decision
MERA=Maine Research Array
BOEM=Bureau of Ocean Energy Management
Design Semisubmersible Barge
Build Semisubmersible Barge
MERA Environmental Assessments
MERA Construction and Installation
BOEM
B1
Renewable Energy Process: Leasing to WTG Installation
